




RISE WV

JOINT COMMITTEE ON FLOODING
INDIVIDUAL COUNTY UPDATE

04/30/19




HOUSING PROCESS

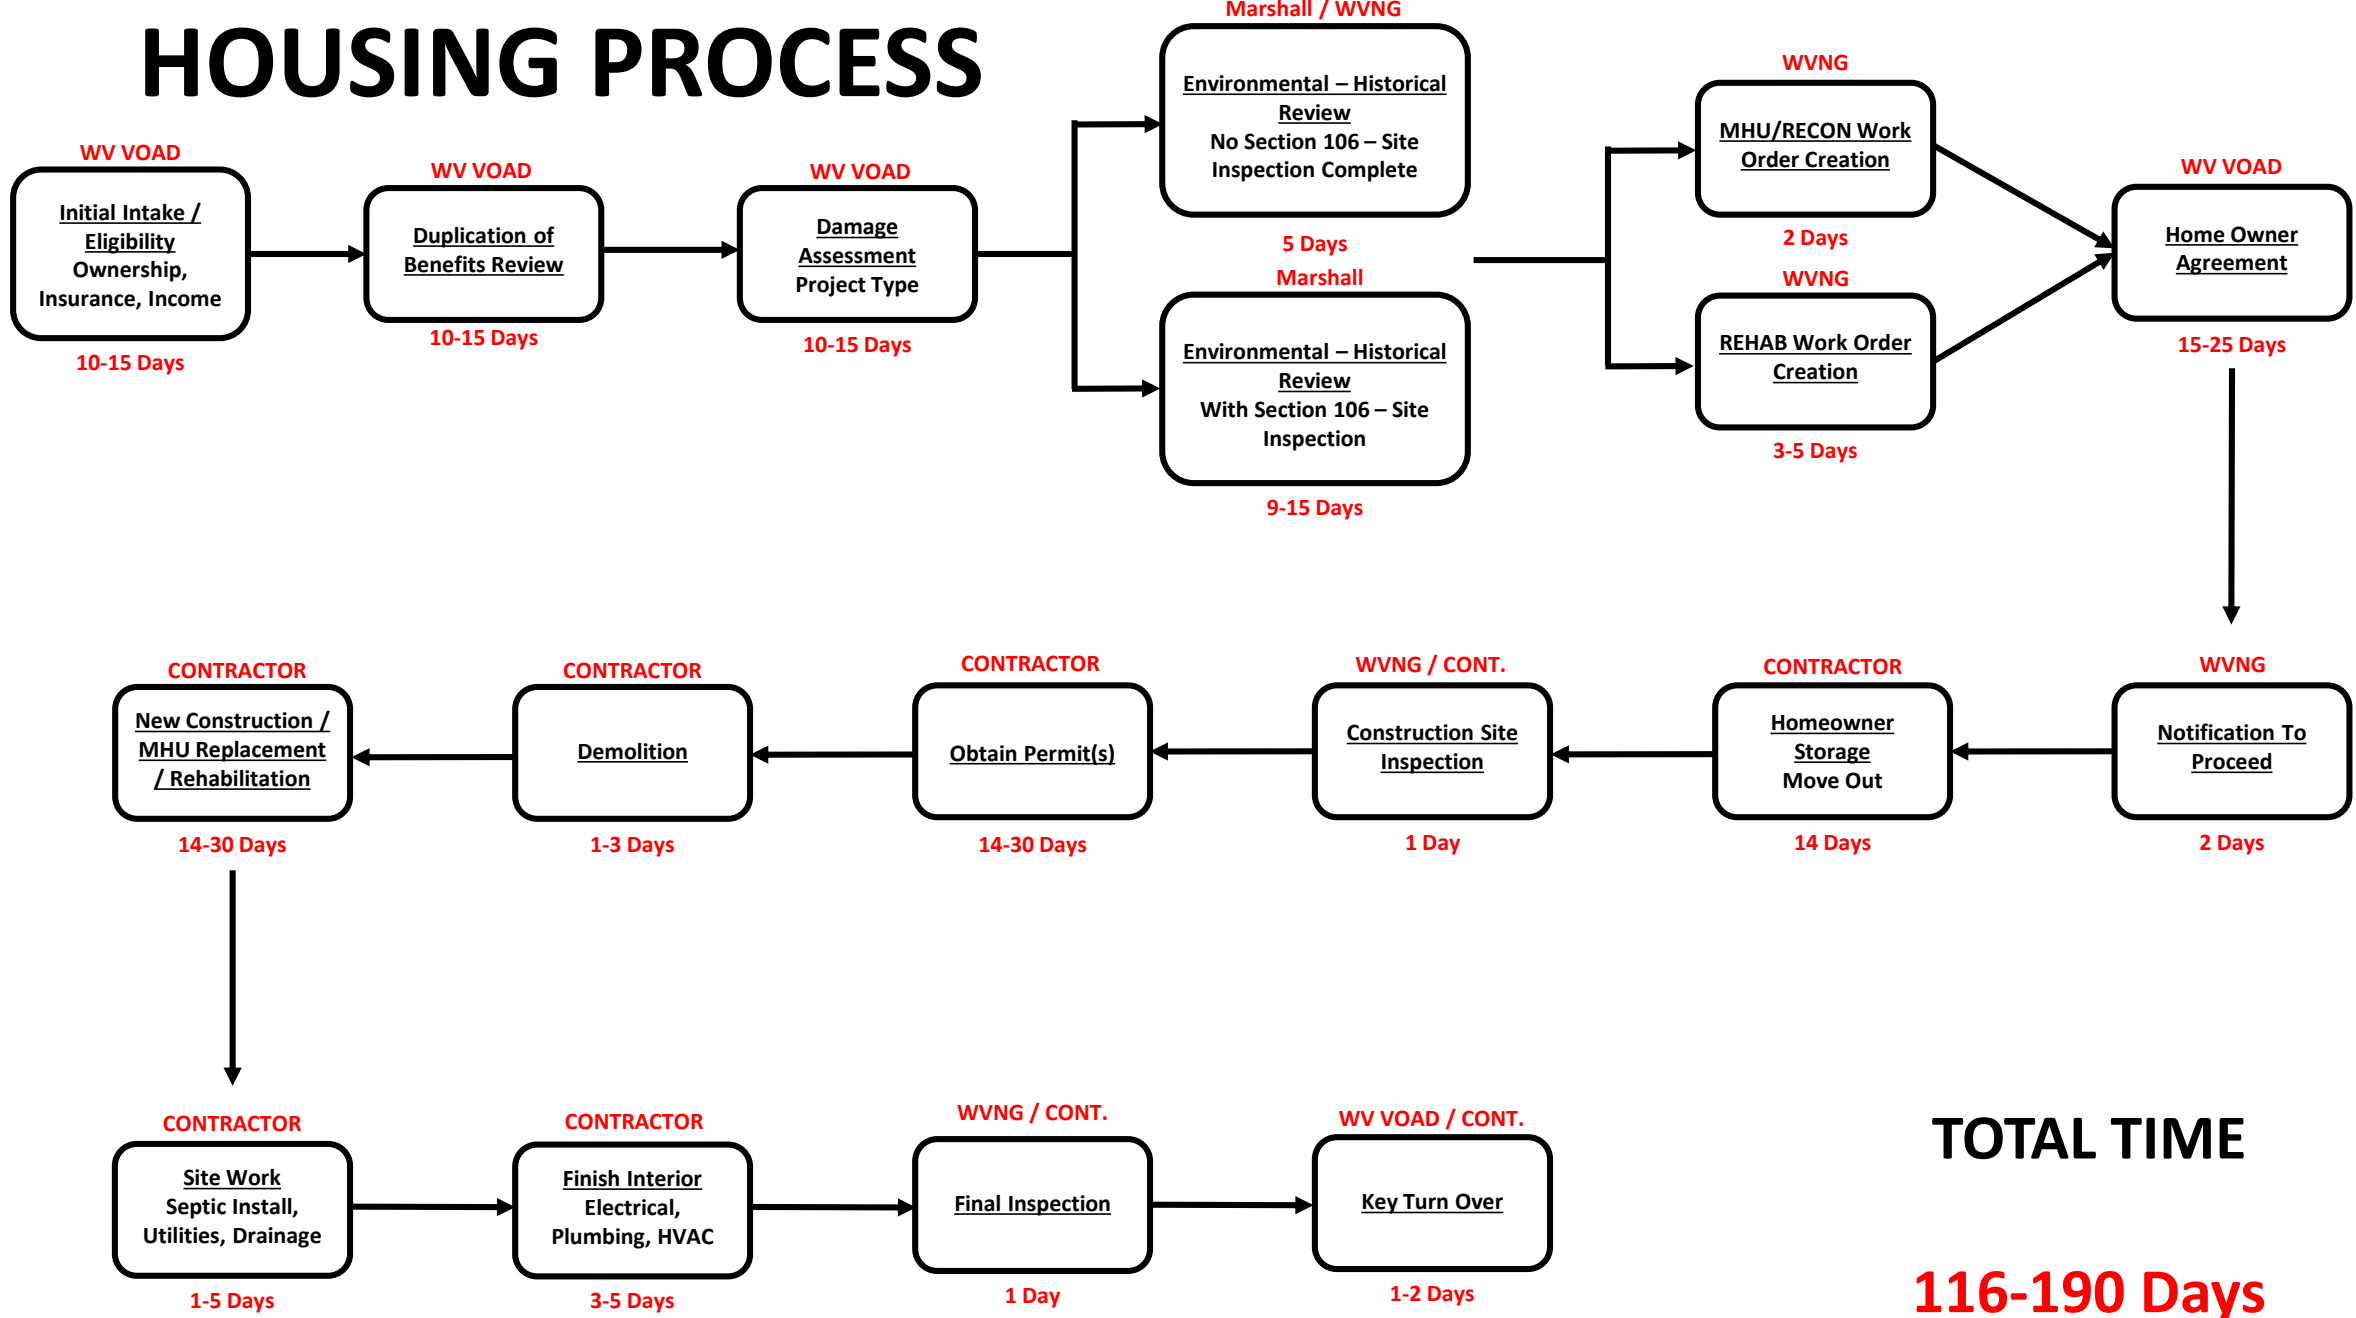

TOTAL TIME
116-190 Days

SLUM & BLIGHT DEMOLITION PROCESS

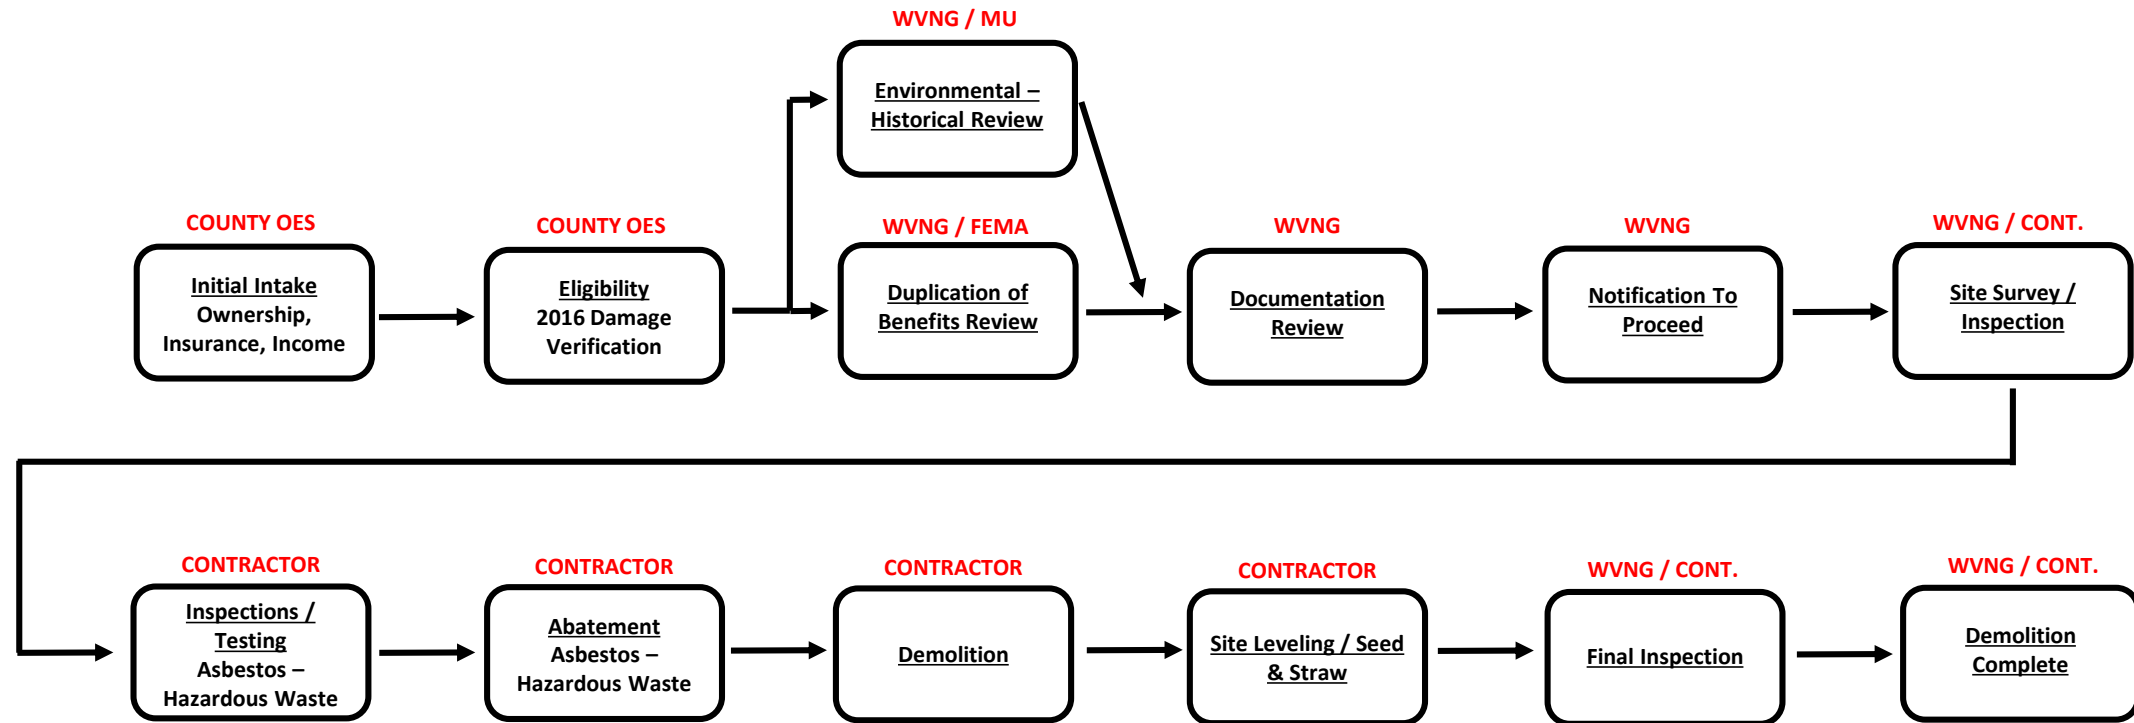

Housing Construction Total

	GRNBR	KAN	CLAY	Nicholas	Fayette	Webster	Roane	Summers	Jackson	Lincoln	Monroe	Pocahont	12 County
CONSTRUCTION TYPE	TOTAL	TOTAL	TOTAL	TOTAL	TOTAL	TOTAL	TOTAL	TOTAL	TOTAL	TOTAL	TOTAL	TOTAL	Total
RECONSTRUCTION	64	54	27	41	27	9	8	4	3	1	2	1	
REHABILITATION	45	9	5	12	14	6	2	3	0	0	1	1	
MOBILE HOME UNIT	13	23	41	13	3	7	3	2	1	5	0	1	
UNASSIGNED	3	6	4	0	1	0	0	0	0	0	0	0	
County Total	125	92	77	66	45	22	13	9	4	6	3	3	465

Housing Construction Completed


	Grnbr	Kan	Clay	Nicholas	Fayette	Webster	Roane	Summers	Jackson	Lincoln	Monroe	Pocahon	12 County
CONSTRUCTION TYPE	COMPL	COMPL	COMPL	COMPL	COMPL	COMPL	COMPL	COMPL	COMPL	COMPL	COMPL	COMPL	Total
RECONSTRUCTION	1	1	0	1	0	0	0	0	0	0	0	0	
REHABILITATION	0	0	0	0	0	0	0	0	0	0	0	0	
MOBILE HOME UNIT	3	8	12	12	4	5	1	0	0	1	0	0	
UNASSIGNED	0	0	0	0	0	0	0	0	0	0	0	0	
County Total	4	9	12	13	4	5	1	0	0	1	0	0	49

Greenbrier County - Construction

Greenbrier County currently has 15 Cases in the early, or “Under Contract” stage of the Construction Process. The “Under Contract” stage consists of activities including; Receiving the Notification to Proceed, Construction Site Inspections, Permitting, and conducting Asbestos Inspections and Abatements.

Greenbrier County also has two (2) Cases in the “Active Construction” stage of the Construction Process. “Active Construction” consists of activities including; Removal and Replacement of Septic Systems, Demolition of Damaged Structure, and New Construction. This process concludes when all construction activities have been completed and the home has passed a Final Inspection certifying that it is ready for re-occupation by the Homeowner.

	CONSTRUCTION	TOTAL	COMPL
GREENBRIER	RECONSTRUCTION	49	1
	REHABILITATION	42	0
	MHU	12	2
	UNASSIGNED	2	0
	TOTALS	105	3

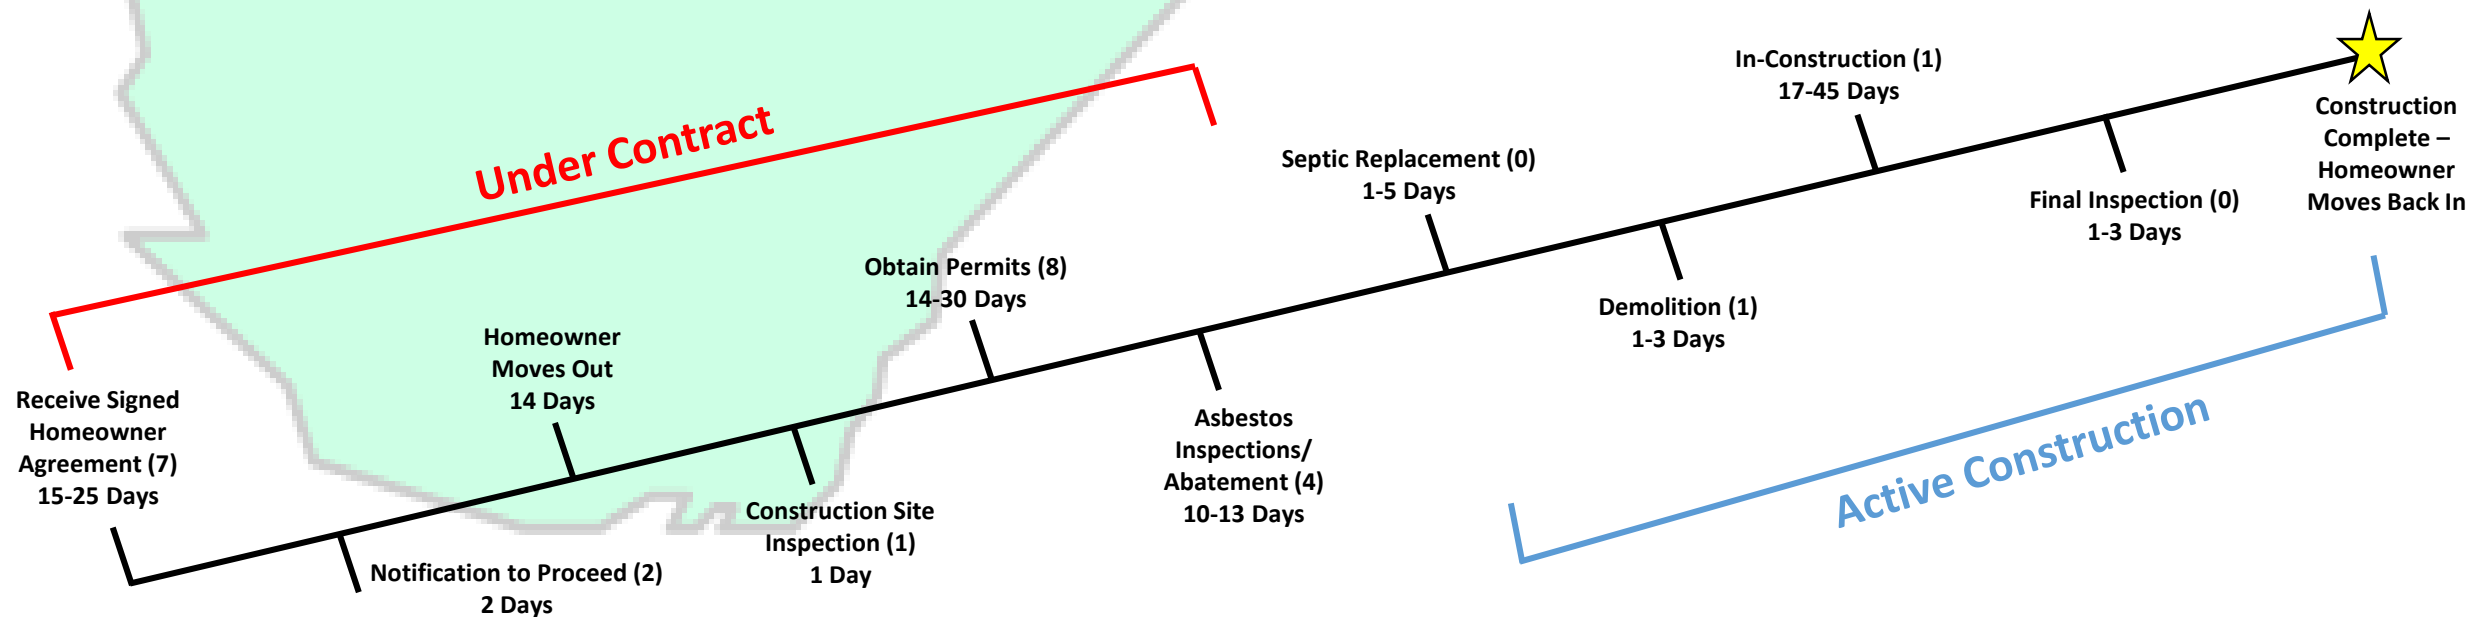


Greenbrier County – Case Management

Case Managers continue to assist the Residents of Greenbrier County by helping them through the “Eligibility” process. Currently, there are (89) Cases going through the “Eligibility” process, which includes; Initial Application Intake, Damage Assessments to determine the type of work needed, Duplication of Benefits review, and testing for Lead Based Paints.

After “Eligibility” has been determined, Case Managers will begin the “Final Processing” of each Case file. Currently, Greenbrier County has (48) going through this process, which includes the following activities; Environmental Reviews, construction Work Order development, and a Quality Control review. Once the Quality Control review is completed, the Case File will be ready for a Homeowner Agreement, which is the last stage in the Case Management process.

	CASE STATUS	TOTAL
GREENBRIER	INITIAL INTAKE	85
	DAMAGE ASSESSMENT	2
	DOB REVIEW	1
	LBP REVIEW	1
	EHP / ERR REVIEW	27
	PACKET QA/QC	1
	WORK ORDER	14
	HOMEOWNER AGREEMENT	6
	PROCESS COMPLETE	19

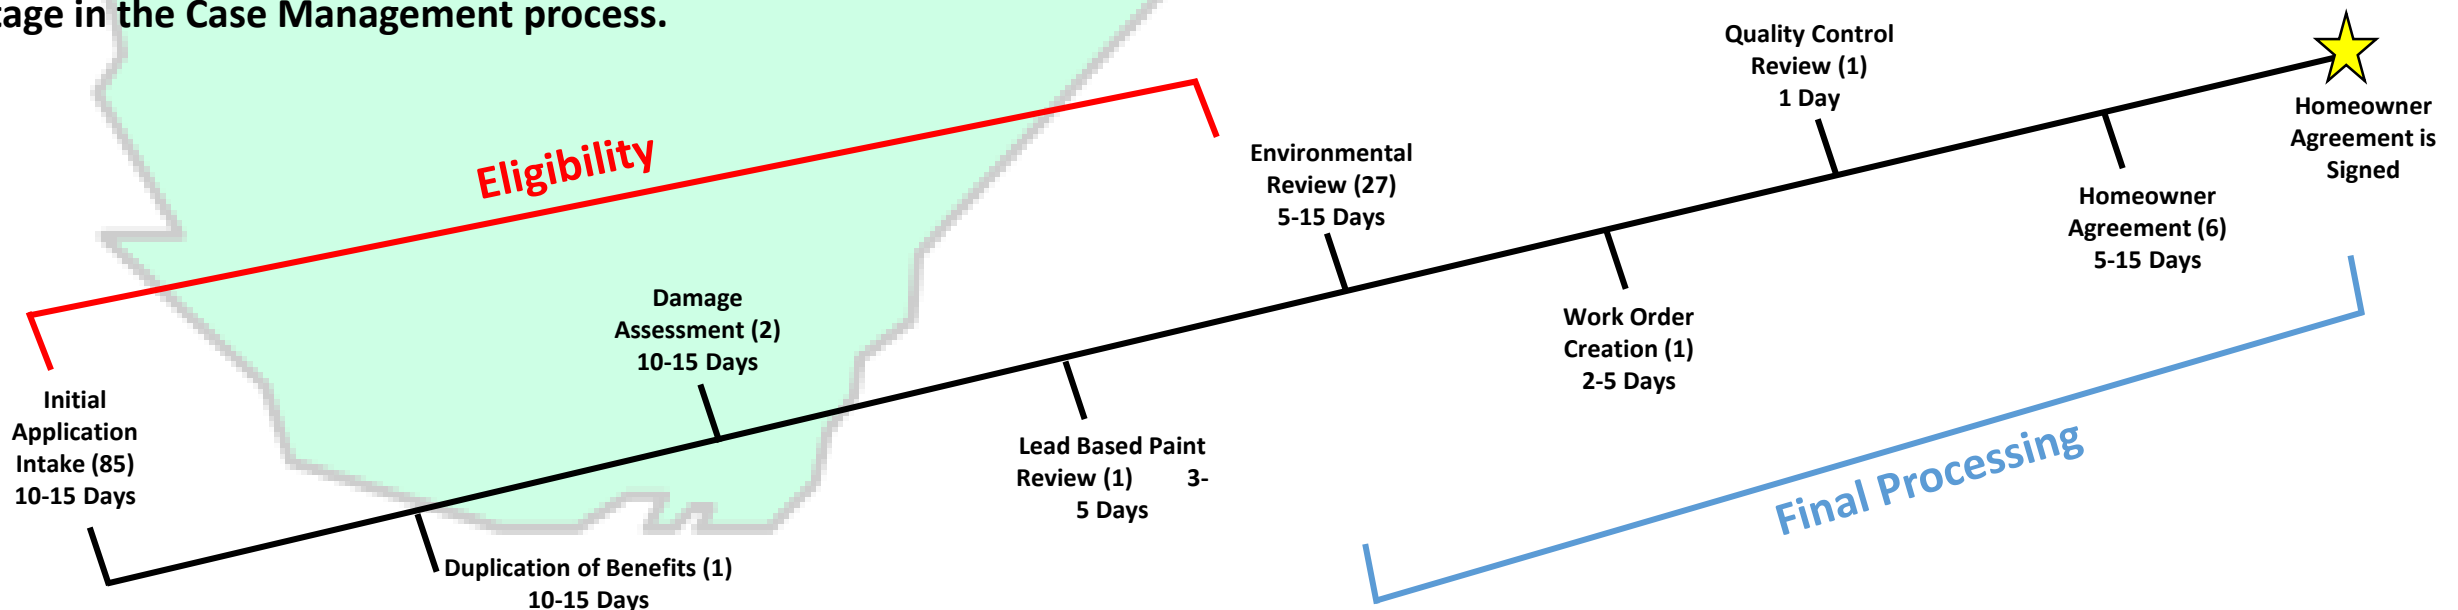


Kanawha County - Construction

Kanawha County currently has 11 Cases in the early, or “Under Contract” stage of the Construction Process. The “Under Contract” stage consists of activities including; Receiving the Notification to Proceed, Construction Site Inspections, Permitting, and conducting Asbestos Inspections and Abatements.

Kanawha County also has three (3) Cases in the “Active Construction” stage of the Construction Process. “Active Construction” consists of activities including; Removal and Replacement of Septic Systems, Demolition of Damaged Structure, and New Construction. This process concludes when all construction activities have been completed and the home has passed a Final Inspection certifying that it is ready for re-occupation by the Homeowner.

	CONSTRUCTION	TOTAL	COMPL
KANAWHA	RECONSTRUCTION	44	1
	REHABILITATION	7	0
	MHU	20	7
	UNASSIGNED	4	0
	TOTALS	75	8

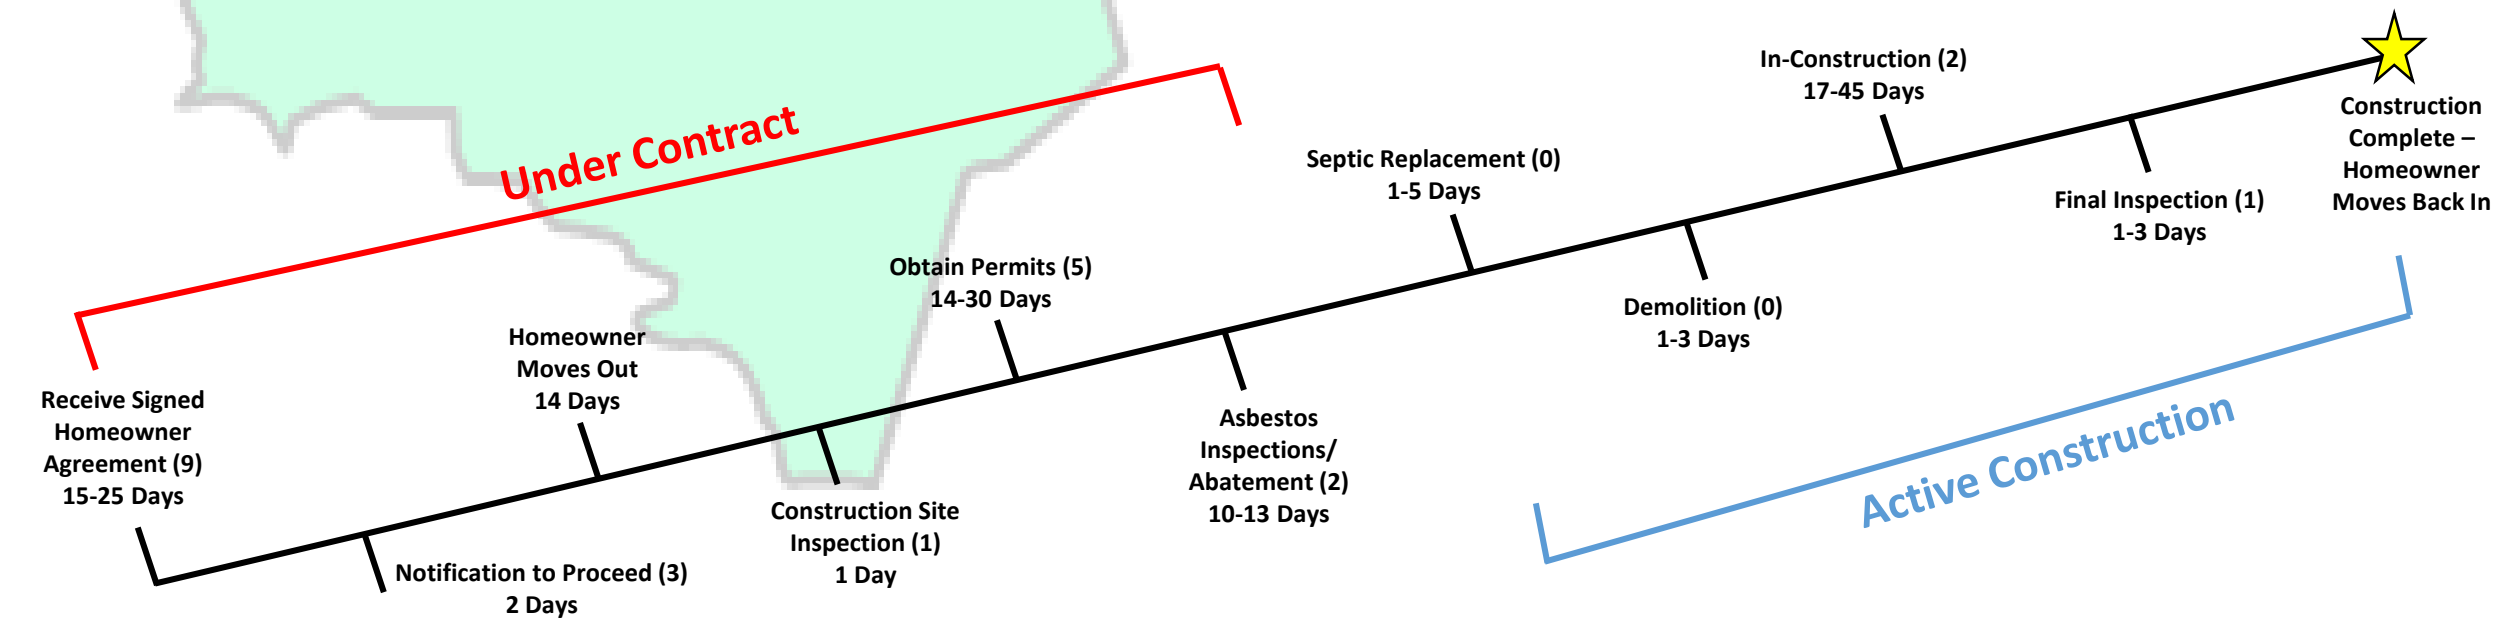


Kanawha County – Case Management

Case Managers continue to assist the Residents of Kanawha County by helping them through the “Eligibility” process. Currently, there are (46) Cases going through the “Eligibility” process, which includes; Initial Application Intake, Damage Assessments to determine the type of work needed, Duplication of Benefits review, and testing for Lead Based Paints.

After “Eligibility” has been determined, Case Managers will begin the “Final Processing” of each Case file. Currently, Kanawha County has (28) going through this process, which includes the following activities; Environmental Reviews, construction Work Order development, and a Quality Control review. Once the Quality Control review is completed, the Case File will be ready for a Homeowner Agreement, which is the last stage in the Case Management process.

	CASE STATUS	TOTAL
KANAWHA	INITIAL INTAKE	42
	DAMAGE ASSESSMENT	0
	DOB REVIEW	4
	LBP REVIEW	0
	EHP / ERR REVIEW	11
	PACKET QA/QC	1
	WORK ORDER	3
	HOMEOWNER AGREEMENT	13
	PROCESS COMPLETE	16

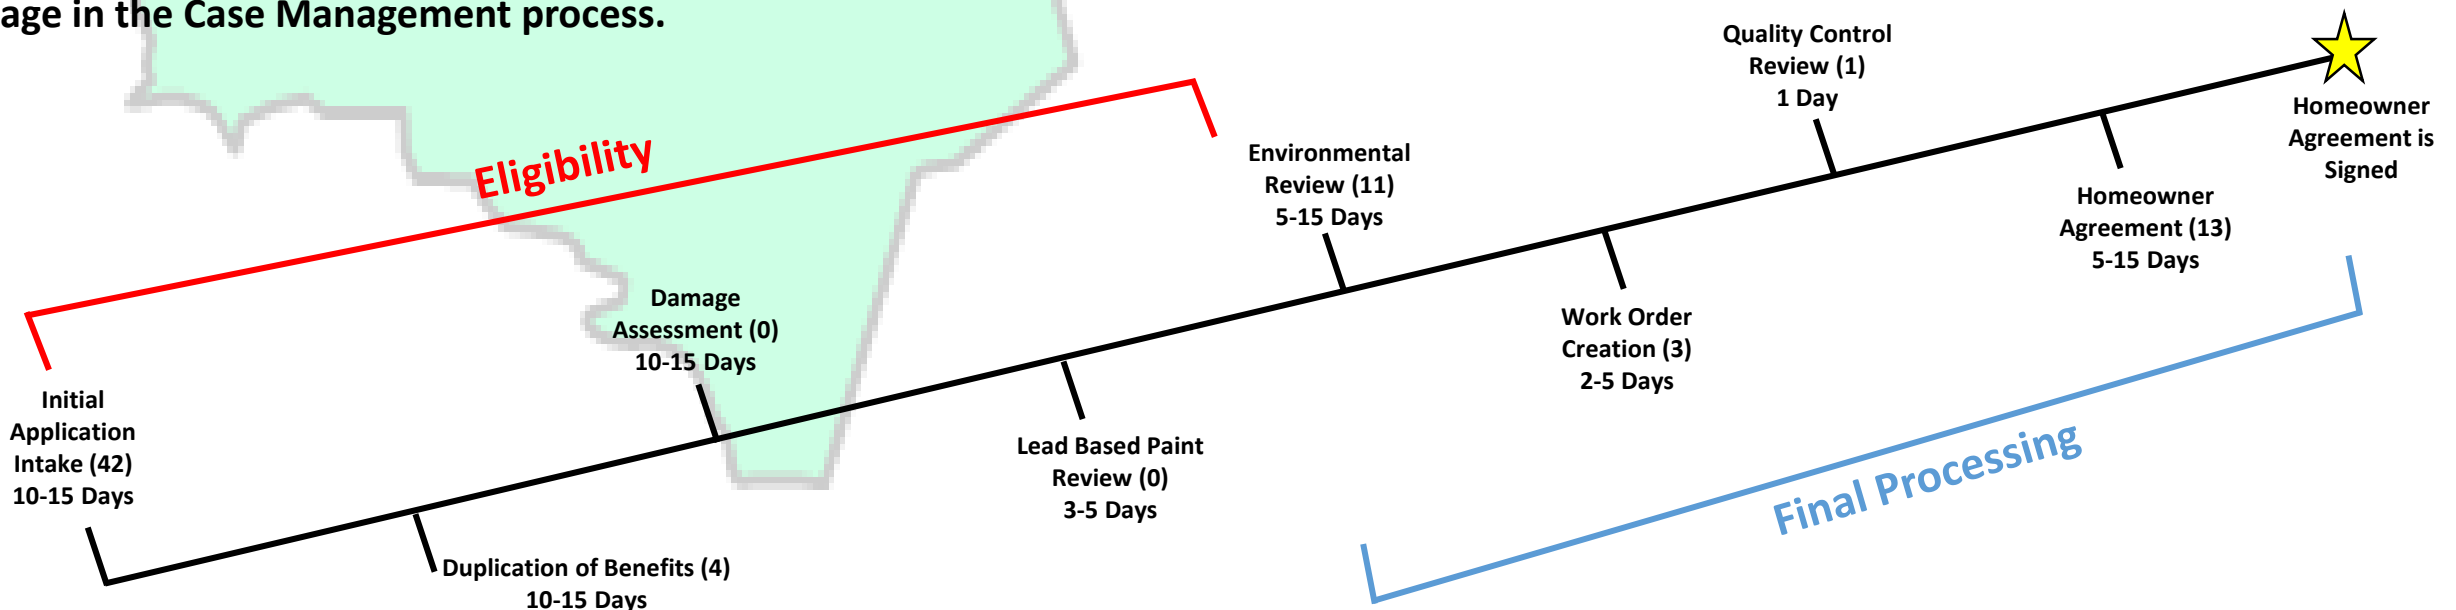


Clay County - Construction

Clay County currently has eight (8) Cases in the early, or “Under Contract” stage of the Construction Process. The “Under Contract” stage consists of activities including; Receiving the Notification to Proceed, Construction Site Inspections, Permitting, and conducting Asbestos Inspections and Abatements.

Clay County also has zero (0) Cases in the “Active Construction” stage of the Construction Process. “Active Construction” consists of activities including; Removal and Replacement of Septic Systems, Demolition of Damaged Structure, and New Construction. This process concludes when all construction activities have been completed and the home has passed a Final Inspection certifying that it is ready for re-occupation by the Homeowner.

	CONSTRUCTION	TOTAL	COMPL
CLAY	RECONSTRUCTION	26	0
	REHABILITATION	5	0
	MHU	40	12
	UNASSIGNED	3	0
	TOTALS	74	12

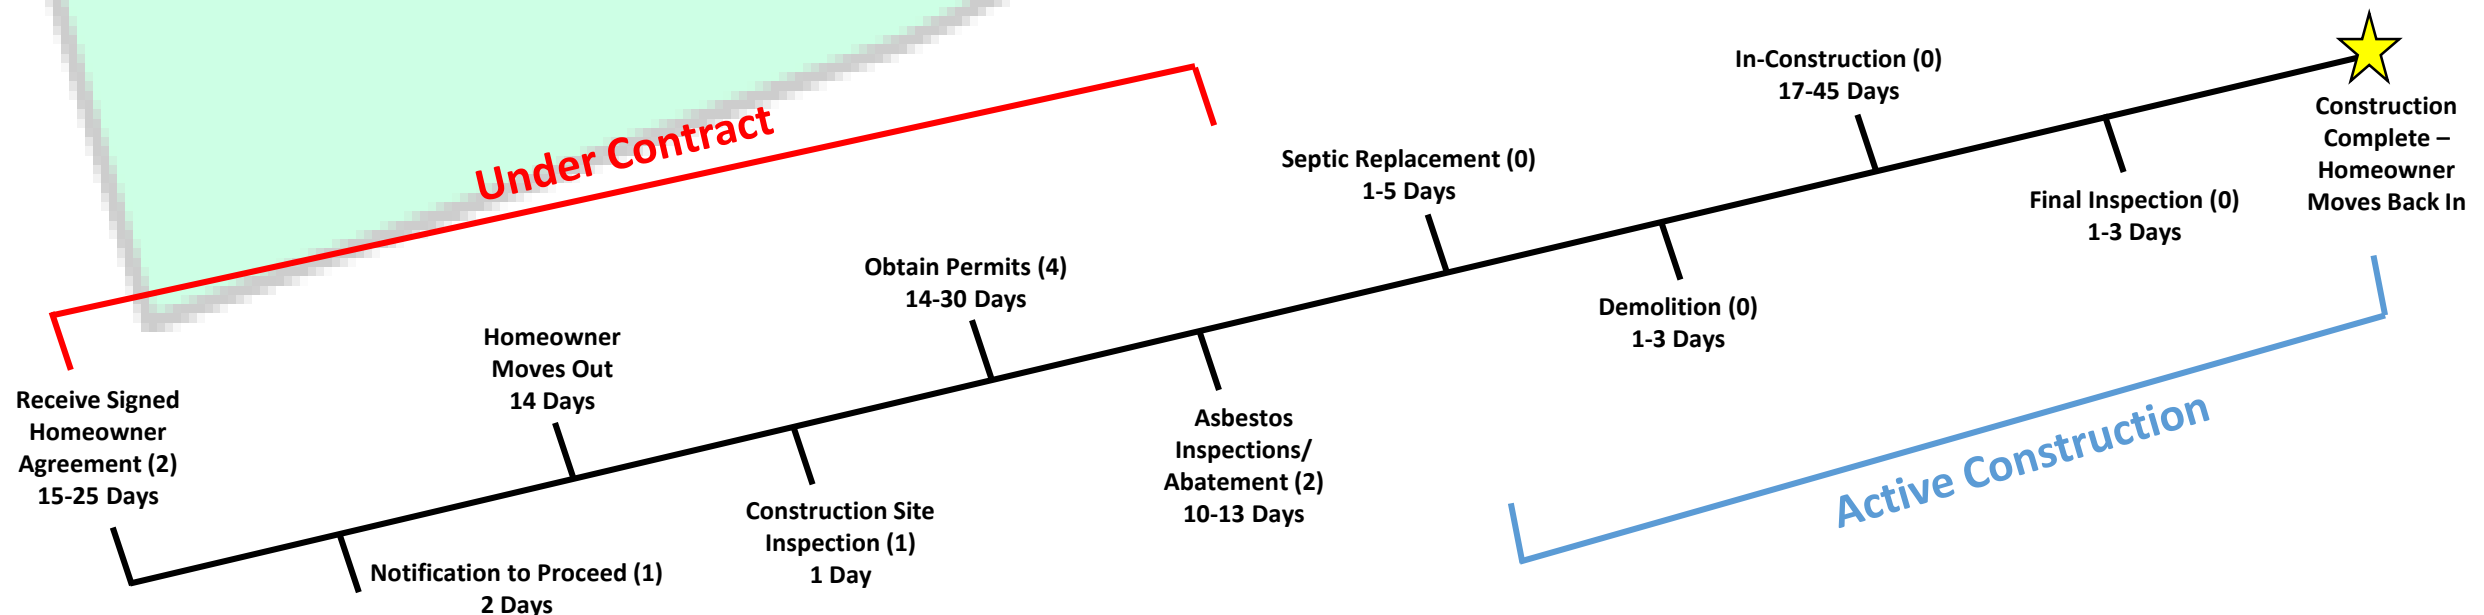


Clay County – Case Management

Case Managers continue to assist the Residents of Clay County by helping them through the “Eligibility” process. Currently, there are (44) Cases going through the “Eligibility” process, which includes; Initial Application Intake, Damage Assessments to determine the type of work needed, Duplication of Benefits review, and testing for Lead Based Paints.

After “Eligibility” has been determined, Case Managers will begin the “Final Processing” of each Case file. Currently, Clay County has (28) going through this process, which includes the following activities; Environmental Reviews, construction Work Order development, and a Quality Control review. Once the Quality Control review is completed, the Case File will be ready for a Homeowner Agreement, which is the last stage in the Case Management process.

	CASE STATUS	TOTAL
CLAY	INITIAL INTAKE	33
	DAMAGE ASSESSMENT	3
	DOB REVIEW	8
	LBP REVIEW	0
	EHP / ERR REVIEW	19
	PACKET QA/QC	2
	WORK ORDER	3
	HOMEOWNER AGREEMENT	4
	PROCESS COMPLETE	8

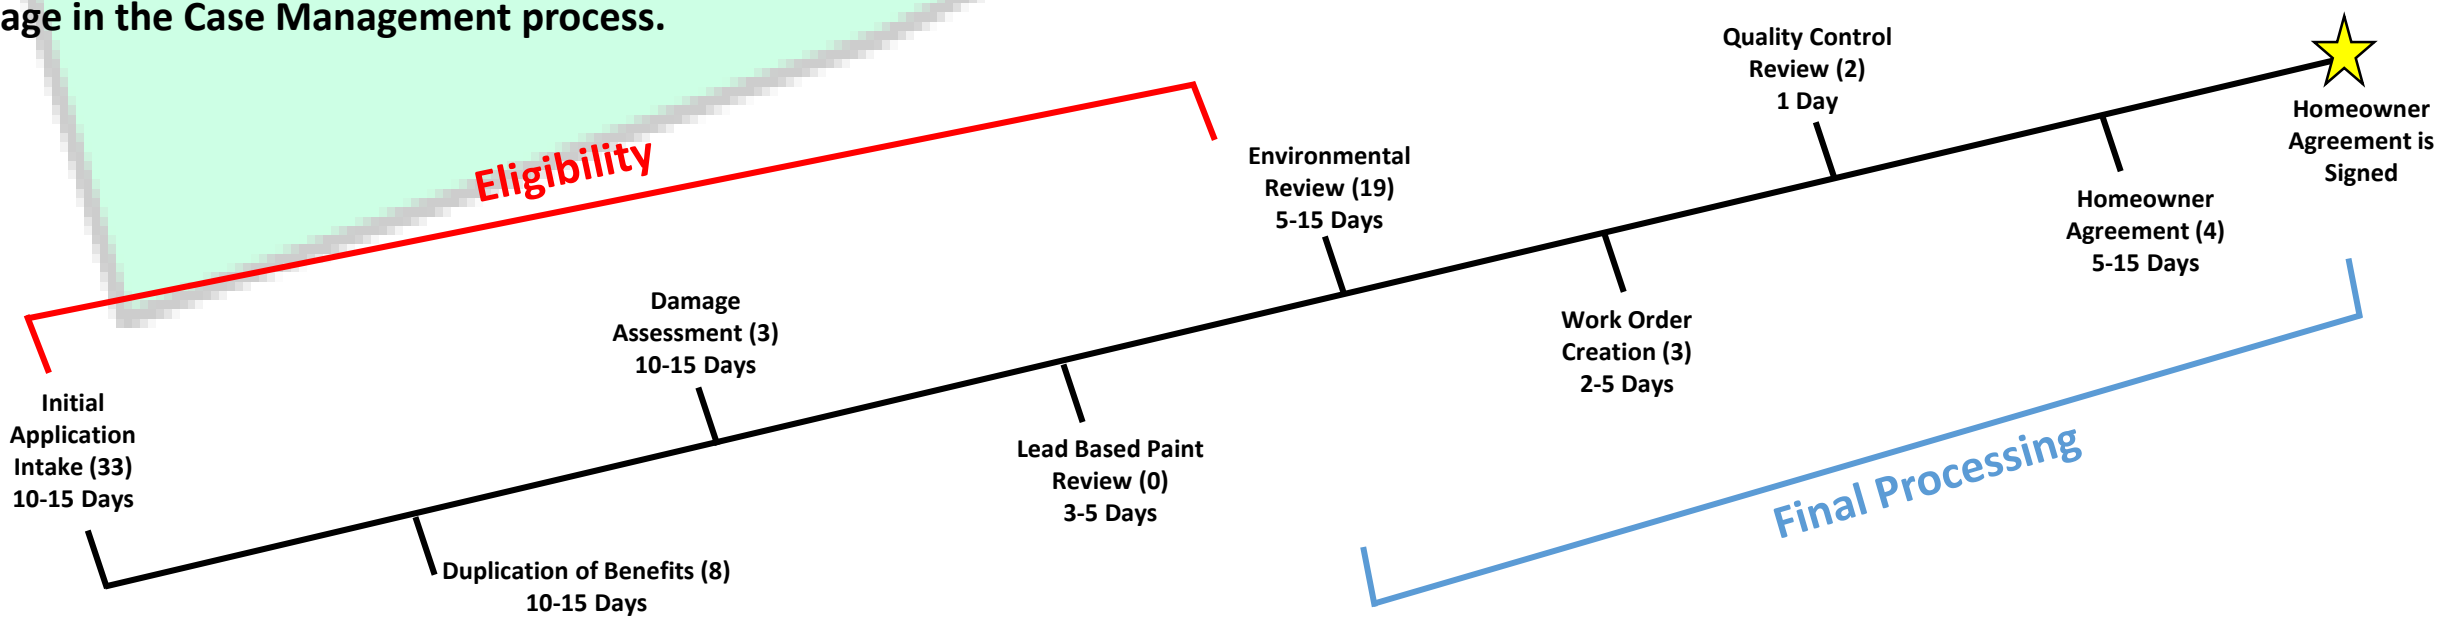


Nicholas County - Construction

Nicholas County currently has nine (9) Cases in the early, or “Under Contract” stage of the Construction Process. The “Under Contract” stage consists of activities including; Receiving the Notification to Proceed, Construction Site Inspections, Permitting, and conducting Asbestos Inspections and Abatements.

Nicholas County also has one (1) Cases in the “Active Construction” stage of the Construction Process. “Active Construction” consists of activities including; Removal and Replacement of Septic Systems, Demolition of Damaged Structure, and New Construction. This process concludes when all construction activities have been completed and the home has passed a Final Inspection certifying that it is ready for re-occupation by the Homeowner.

	CONSTRUCTION	TOTAL	COMPL
NICHOLAS	RECONSTRUCTION	35	1
	REHABILITATION	12	0
	MHU	10	12
	UNASSIGNED	0	0
	TOTALS	57	13

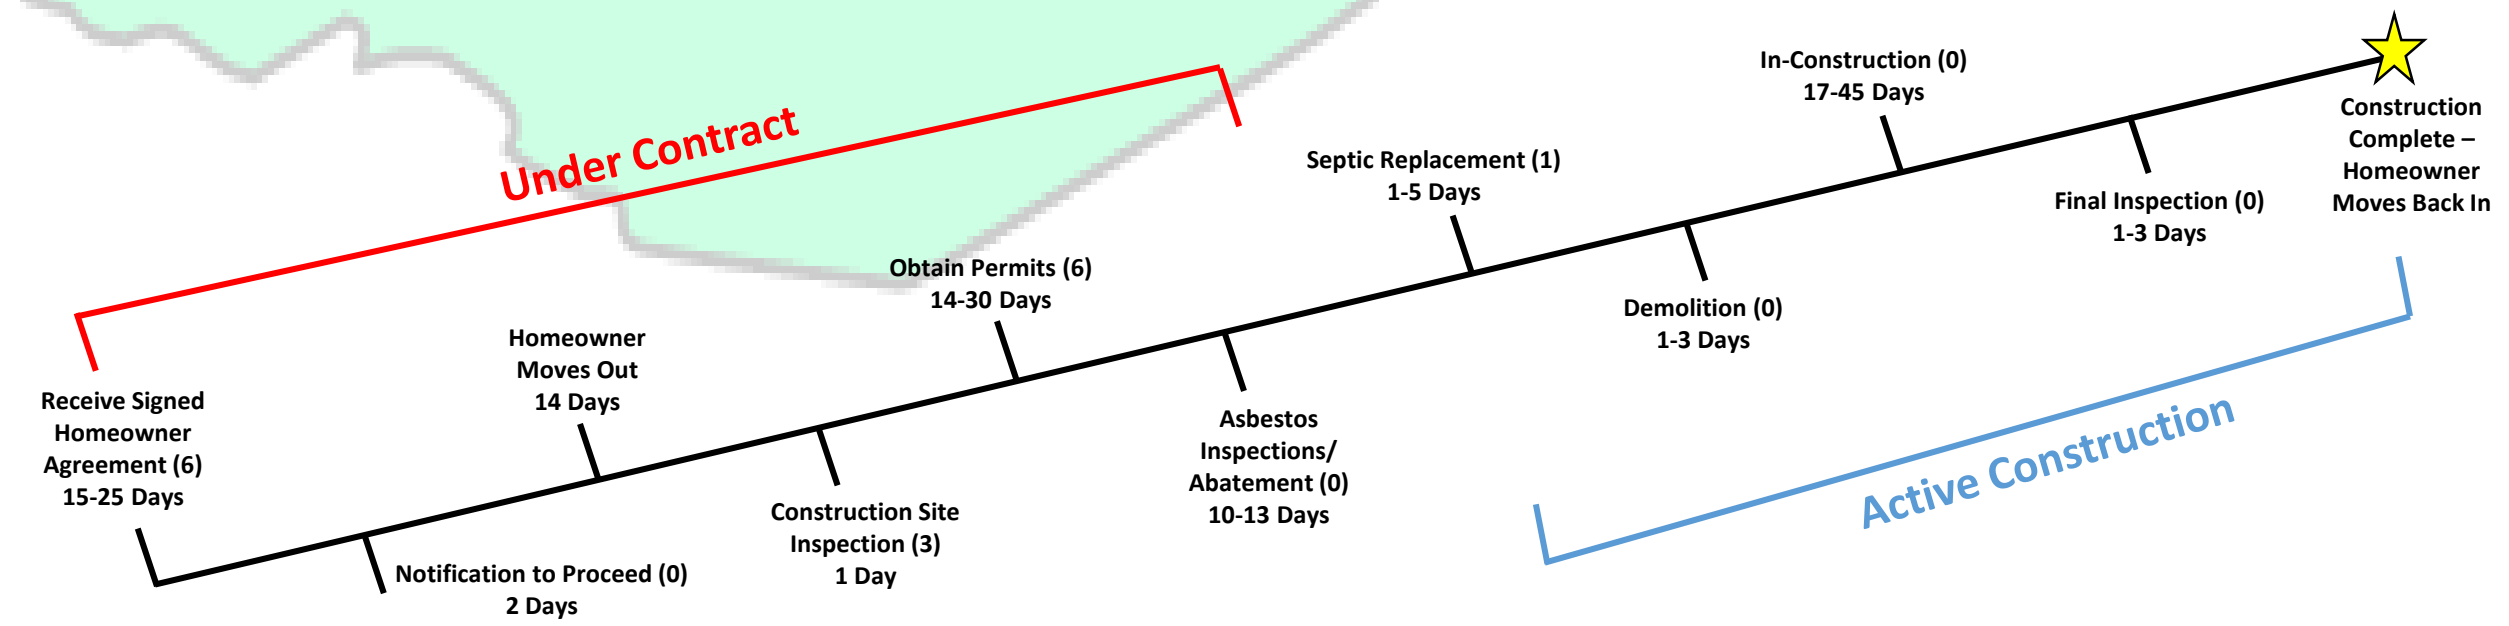


Nicholas County – Case Management

Case Managers continue to assist the Residents of Nicholas County by helping them through the “Eligibility” process. Currently, there are (29) Cases going through the “Eligibility” process, which includes; Initial Application Intake, Damage Assessments to determine the type of work needed, Duplication of Benefits review, and testing for Lead Based Paints.

After “Eligibility” has been determined, Case Managers will begin the “Final Processing” of each Case file. Currently, Nicholas County has (24) going through this process, which includes the following activities; Environmental Reviews, construction Work Order development, and a Quality Control review. Once the Quality Control review is completed, the Case File will be ready for a Homeowner Agreement, which is the last stage in the Case Management process.

	CASE STATUS	TOTAL
NICHOLAS	INITIAL INTAKE	28
	DAMAGE ASSESSMENT	0
	DOB REVIEW	1
	LBP REVIEW	0
	EHP / ERR REVIEW	2
	PACKET QA/QC	2
	WORK ORDER	9
	HOMEOWNER AGREEMENT	11
	PROCESS COMPLETE	5

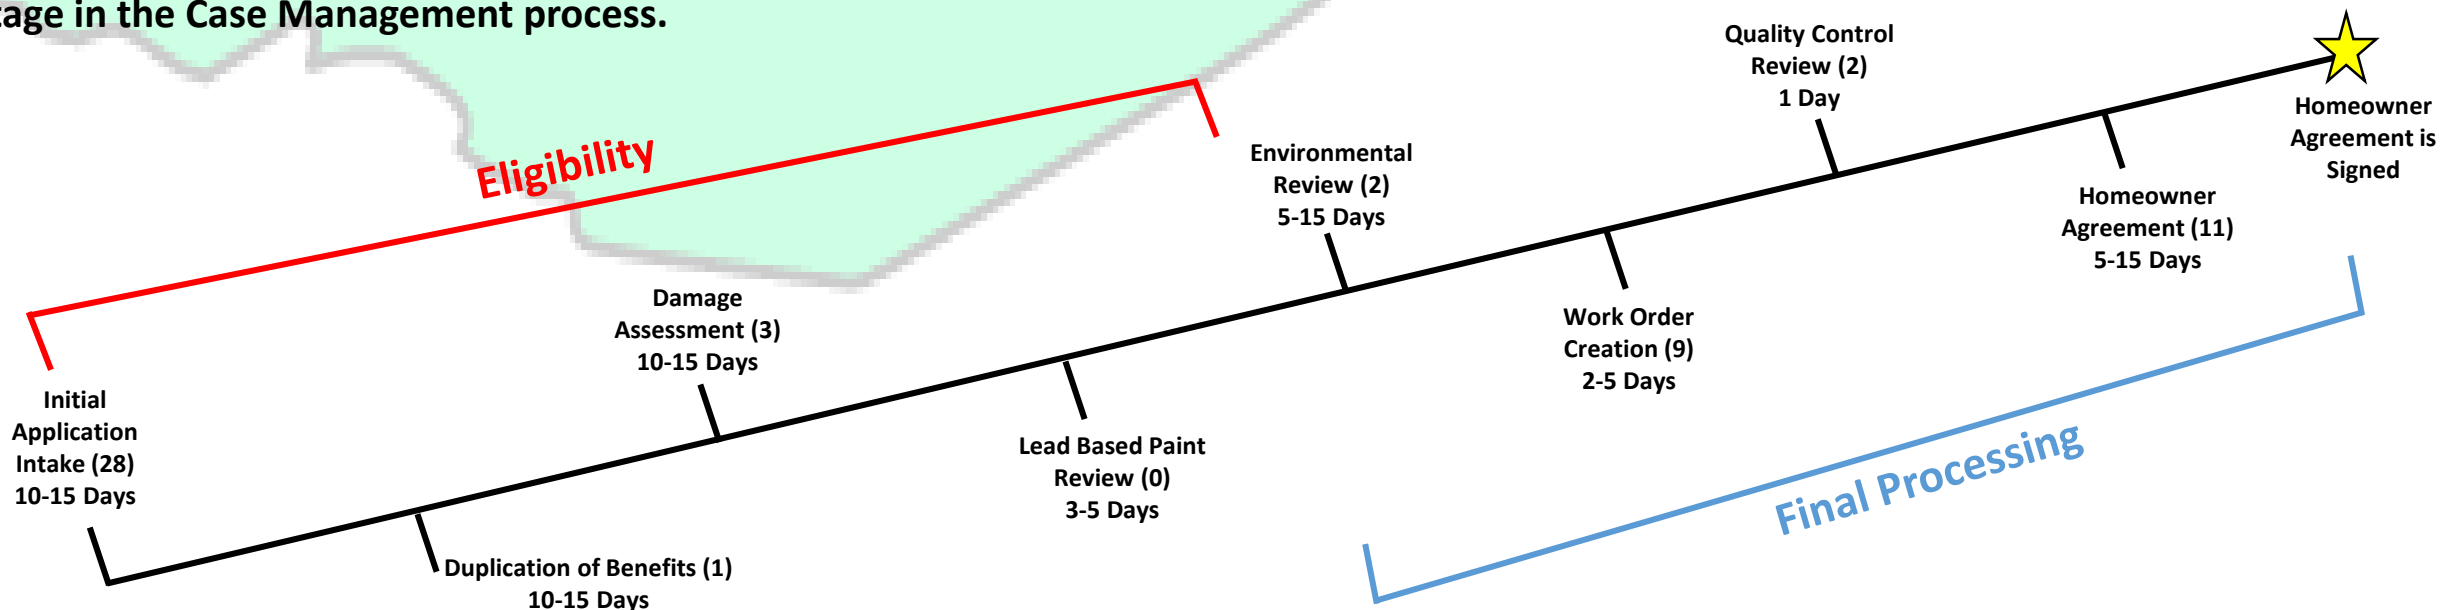


Fayette County - Construction

Fayette County currently has 11 Cases in the early, or “Under Contract” stage of the Construction Process. The “Under Contract” stage consists of activities including; Receiving the Notification to Proceed, Construction Site Inspections, Permitting, and conducting Asbestos Inspections and Abatements.

Fayette County also has zero (0) Cases in the “Active Construction” stage of the Construction Process. “Active Construction” consists of activities including; Removal and Replacement of Septic Systems, Demolition of Damaged Structure, and New Construction. This process concludes when all construction activities have been completed and the home has passed a Final Inspection certifying that it is ready for re-occupation by the Homeowner.

	CONSTRUCTION	TOTAL	COMPL
FAYETTE	RECONSTRUCTION	27	0
	REHABILITATION	13	0
	MHU	3	4
	UNASSIGNED	1	0
	TOTALS	44	4

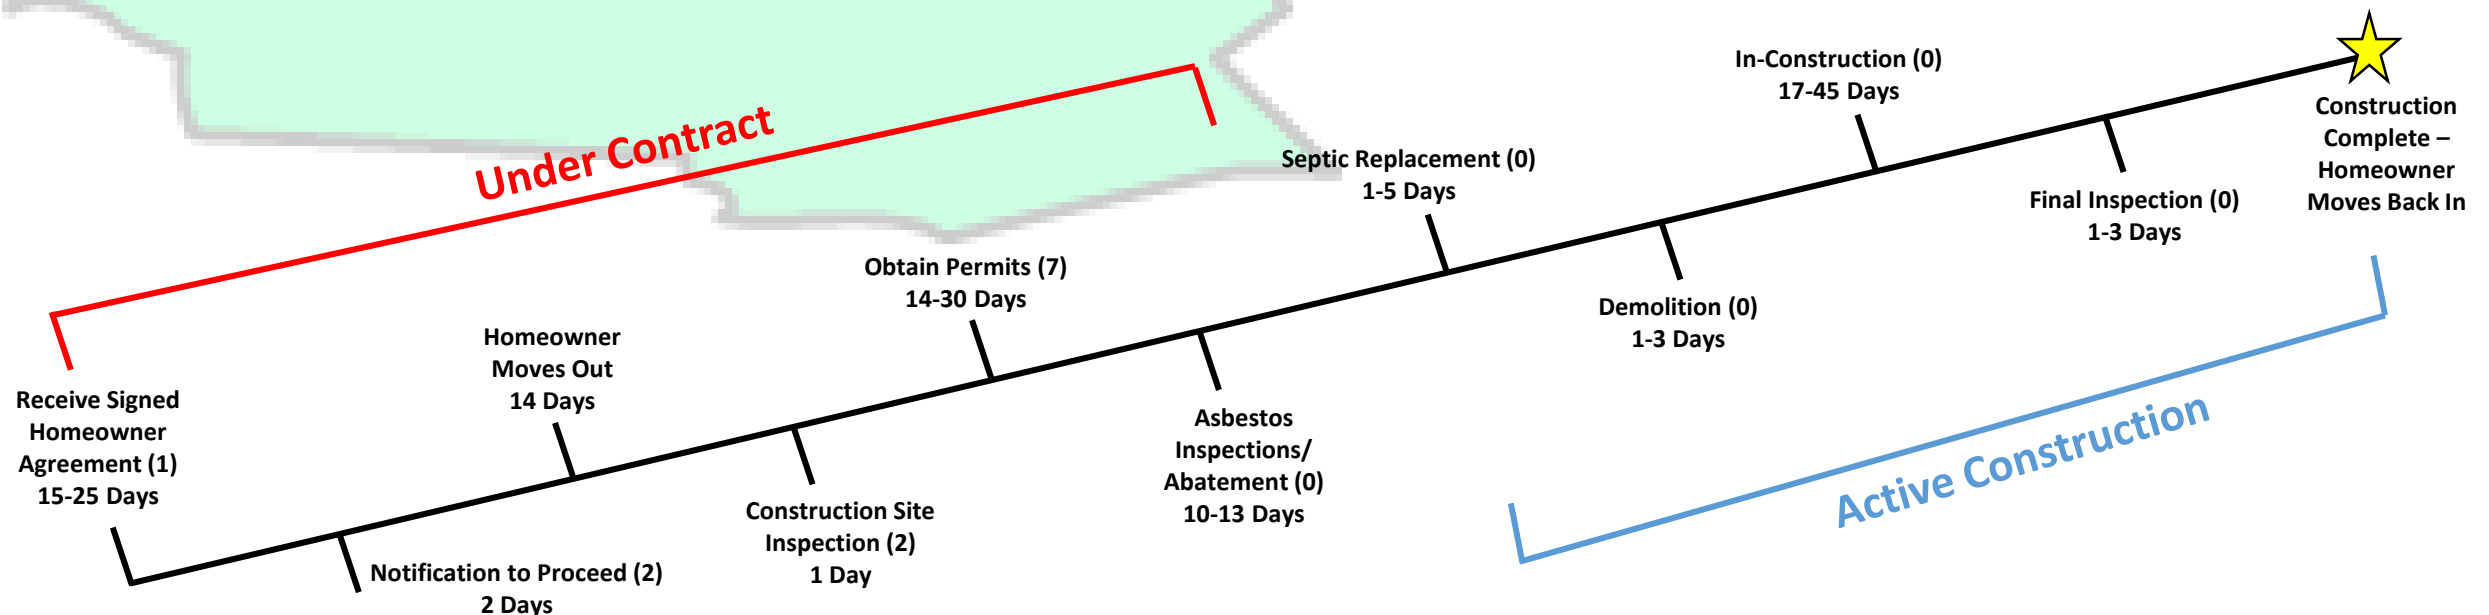


Fayette County – Case Management

Case Managers continue to assist the Residents of Fayette County by helping them through the “Eligibility” process. Currently, there are nine (20) Cases going through the “Eligibility” process, which includes; Initial Application Intake, Damage Assessments to determine the type of work needed, Duplication of Benefits review, and testing for Lead Based Paints.

After “Eligibility” has been determined, Case Managers will begin the “Final Processing” of each Case file. Currently, Fayette County has (15) going through this process, which includes the following activities; Environmental Reviews, construction Work Order development, and a Quality Control review. Once the Quality Control review is completed, the Case File will be ready for a Homeowner Agreement, which is the last stage in the Case Management process.

	CASE STATUS	TOTAL
FAYETTE	INITIAL INTAKE	20
	DAMAGE ASSESSMENT	0
	DOB REVIEW	0
	LBP REVIEW	0
	EHP / ERR REVIEW	6
	PACKET QA/QC	6
	WORK ORDER	2
	HOMEOWNER AGREEMENT	1
	PROCESS COMPLETE	12

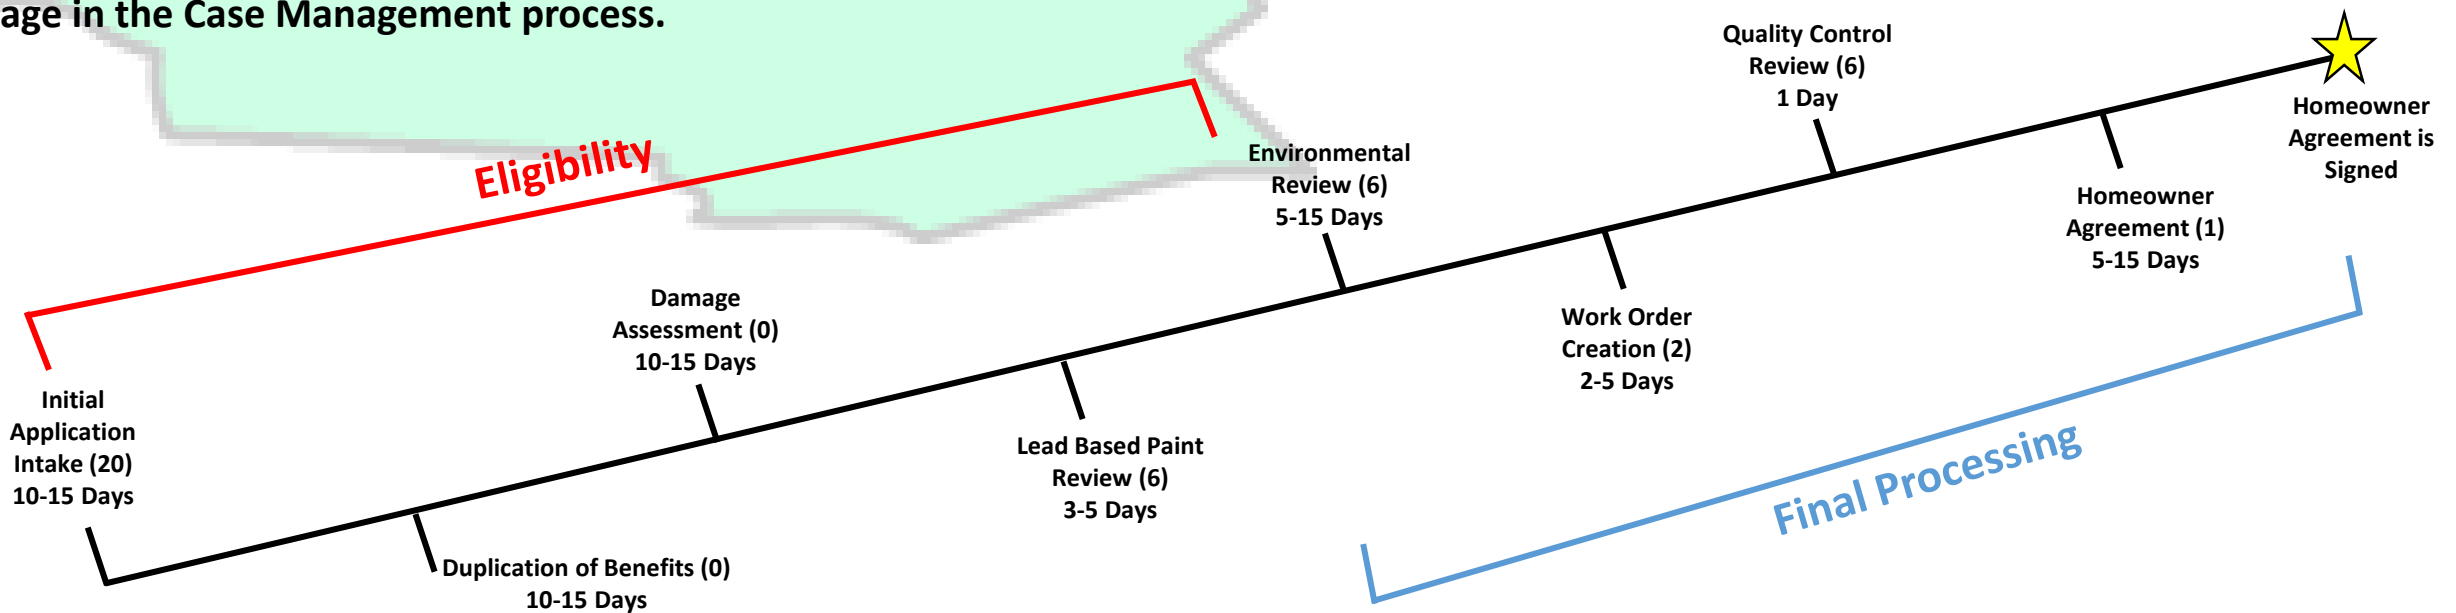


Roane County - Construction

Roane County currently has three (3) Cases in the early, or “Under Contract” stage of the Construction Process. The “Under Contract” stage consists of activities including; Receiving the Notification to Proceed, Construction Site Inspections, Permitting, and conducting Asbestos Inspections and Abatements.

Roane County also has zero (0) Cases in the “Active Construction” stage of the Construction Process. “Active Construction” consists of activities including; Removal and Replacement of Septic Systems, Demolition of Damaged Structure, and New Construction. This process concludes when all construction activities have been completed and the home has passed a Final Inspection certifying that it is ready for re-occupation by the Homeowner.

	CONSTRUCTION	TOTAL	COMPL
ROANE	RECONSTRUCTION	7	0
	REHABILITATION	2	0
	MHU	3	1
	UNASSIGNED	0	0
	TOTALS	12	1

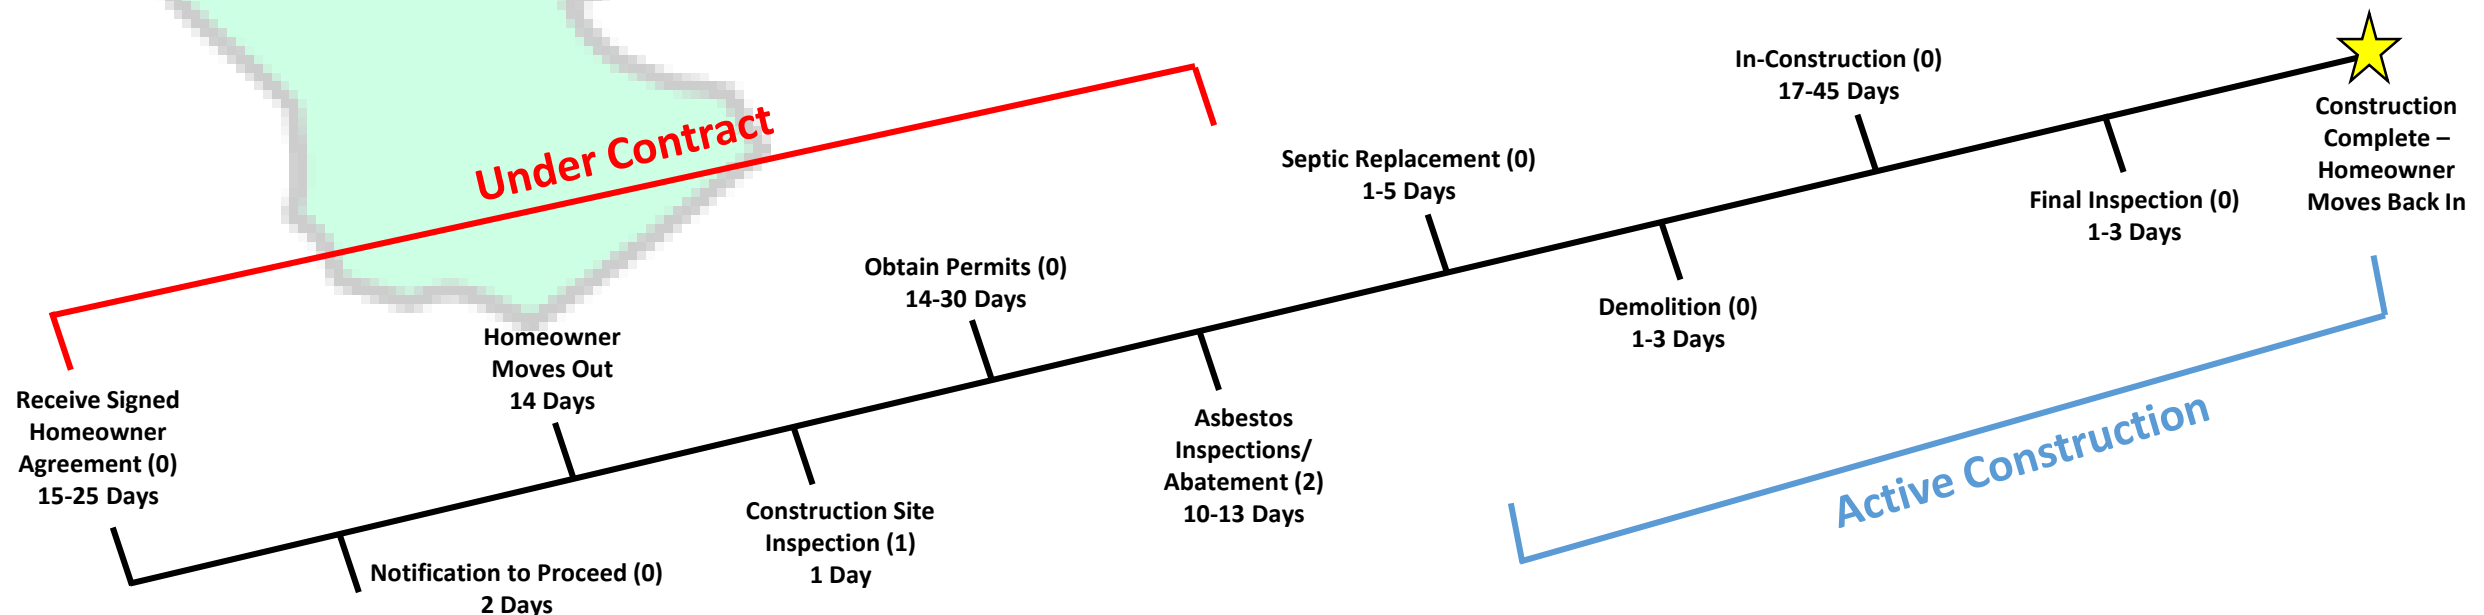


Roane County – Case Management

Case Managers continue to assist the Residents of Roane County by helping them through the “Eligibility” process. Currently, there are three (8) Cases going through the “Eligibility” process, which includes; Initial Application Intake, Damage Assessments to determine the type of work needed, Duplication of Benefits review, and testing for Lead Based Paints.

After “Eligibility” has been determined, Case Managers will begin the “Final Processing” of each Case file. Currently, Roane County has three (4) going through this process, which includes the following activities; Environmental Reviews, construction Work Order development, and a Quality Control review. Once the Quality Control review is completed, the Case File will be ready for a Homeowner Agreement, which is the last stage in the Case Management process.

	CASE STATUS	TOTAL
ROANE	INITIAL INTAKE	6
	DAMAGE ASSESSMENT	1
	DOB REVIEW	1
	LBP REVIEW	0
	EHP / ERR REVIEW	1
	PACKET QA/QC	0
	WORK ORDER	1
	HOMEOWNER AGREEMENT	2
	PROCESS COMPLETE	4

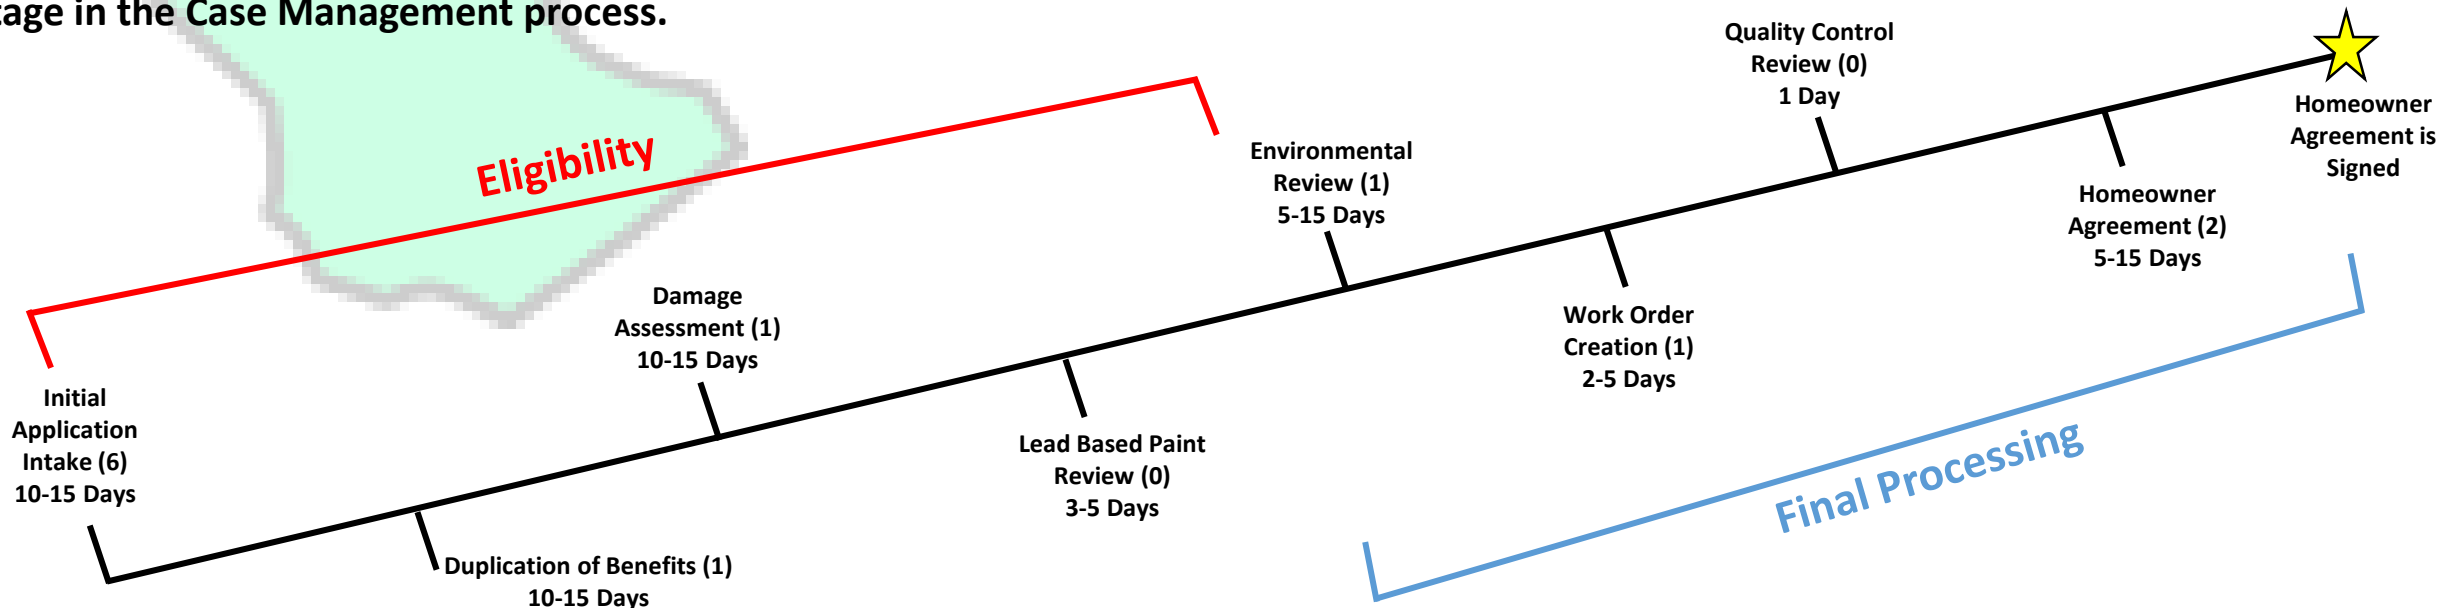


Jackson County - Construction

Jackson County currently has zero (0) Cases in the early, or “Under Contract” stage of the Construction Process. The “Under Contract” stage consists of activities including; Receiving the Notification to Proceed, Construction Site Inspections, Permitting, and conducting Asbestos Inspections and Abatements.

Jackson County also has zero (0) Cases in the “Active Construction” stage of the Construction Process. “Active Construction” consists of activities including; Removal and Replacement of Septic Systems, Demolition of Damaged Structure, and New Construction. This process concludes when all construction activities have been completed and the home has passed a Final Inspection certifying that it is ready for re-occupation by the Homeowner.

	CONSTRUCTION	TOTAL	COMPL
JACKSON	RECONSTRUCTION	3	0
	REHABILITATION	0	0
	MHU	1	0
	UNASSIGNED	0	0
	TOTALS	4	0

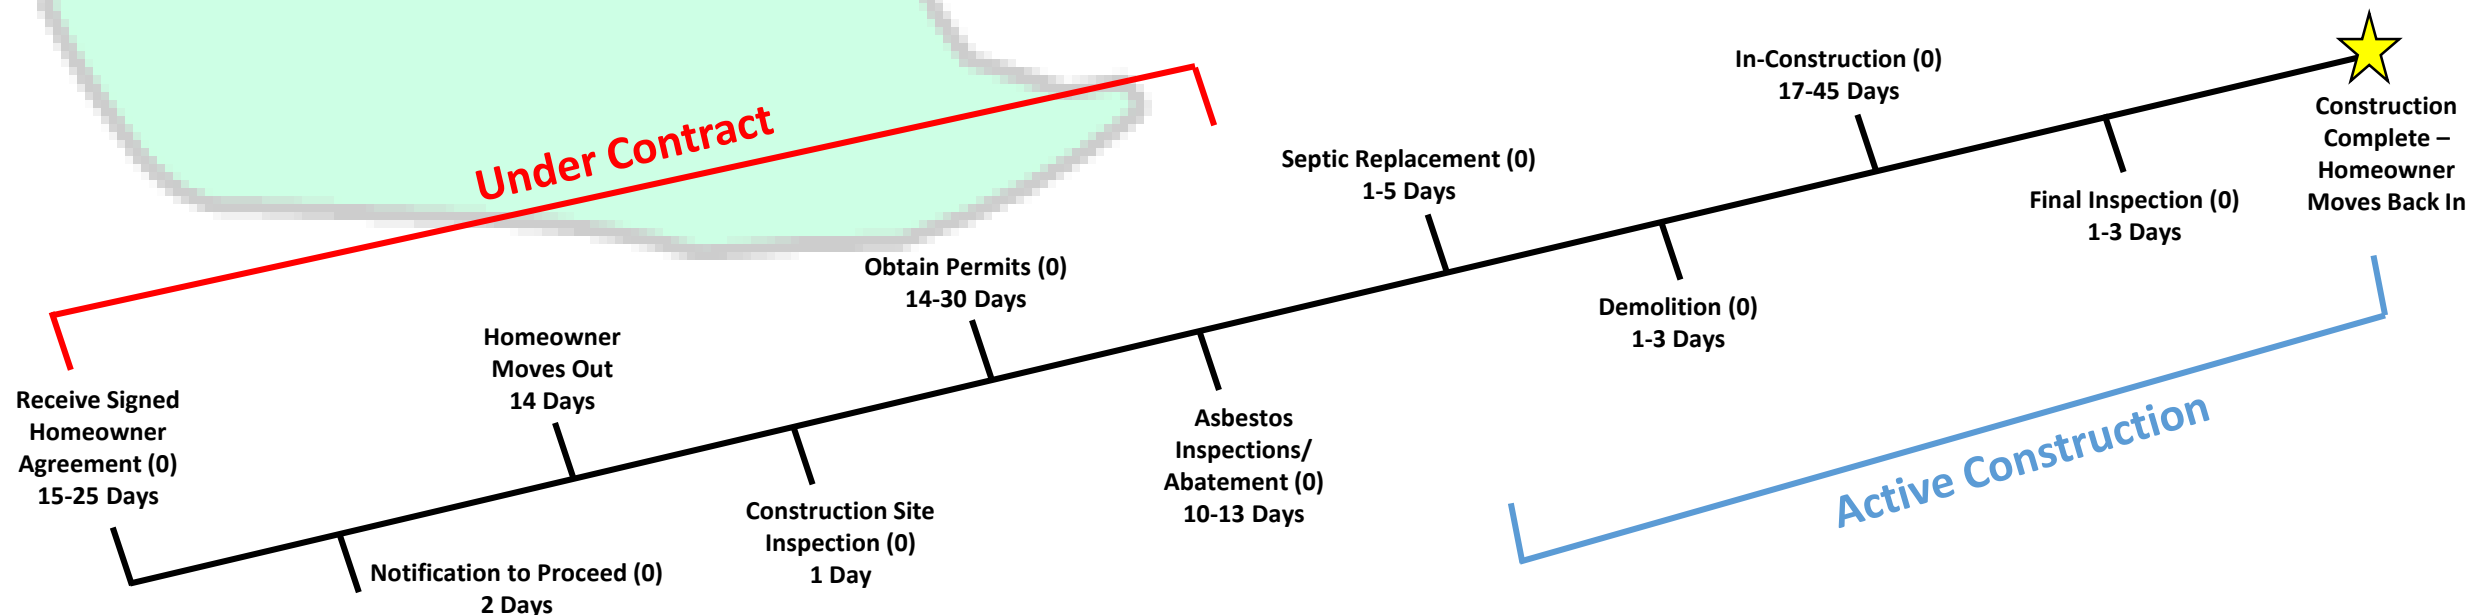


Jackson County – Case Management

Case Managers continue to assist the Residents of Jackson County by helping them through the “Eligibility” process. Currently, there are three (1) Cases going through the “Eligibility” process, which includes; Initial Application Intake, Damage Assessments to determine the type of work needed, Duplication of Benefits review, and testing for Lead Based Paints.

After “Eligibility” has been determined, Case Managers will begin the “Final Processing” of each Case file. Currently, Jackson County has three (2) going through this process, which includes the following activities; Environmental Reviews, construction Work Order development, and a Quality Control review. Once the Quality Control review is completed, the Case File will be ready for a Homeowner Agreement, which is the last stage in the Case Management process.

	CASE STATUS	TOTAL
JACKSON	INITIAL INTAKE	1
	DAMAGE ASSESSMENT	0
	DOB REVIEW	0
	LBP REVIEW	0
	EHP / ERR REVIEW	1
	PACKET QA/QC	0
	WORK ORDER	1
	HOMEOWNER AGREEMENT	1
	PROCESS COMPLETE	0

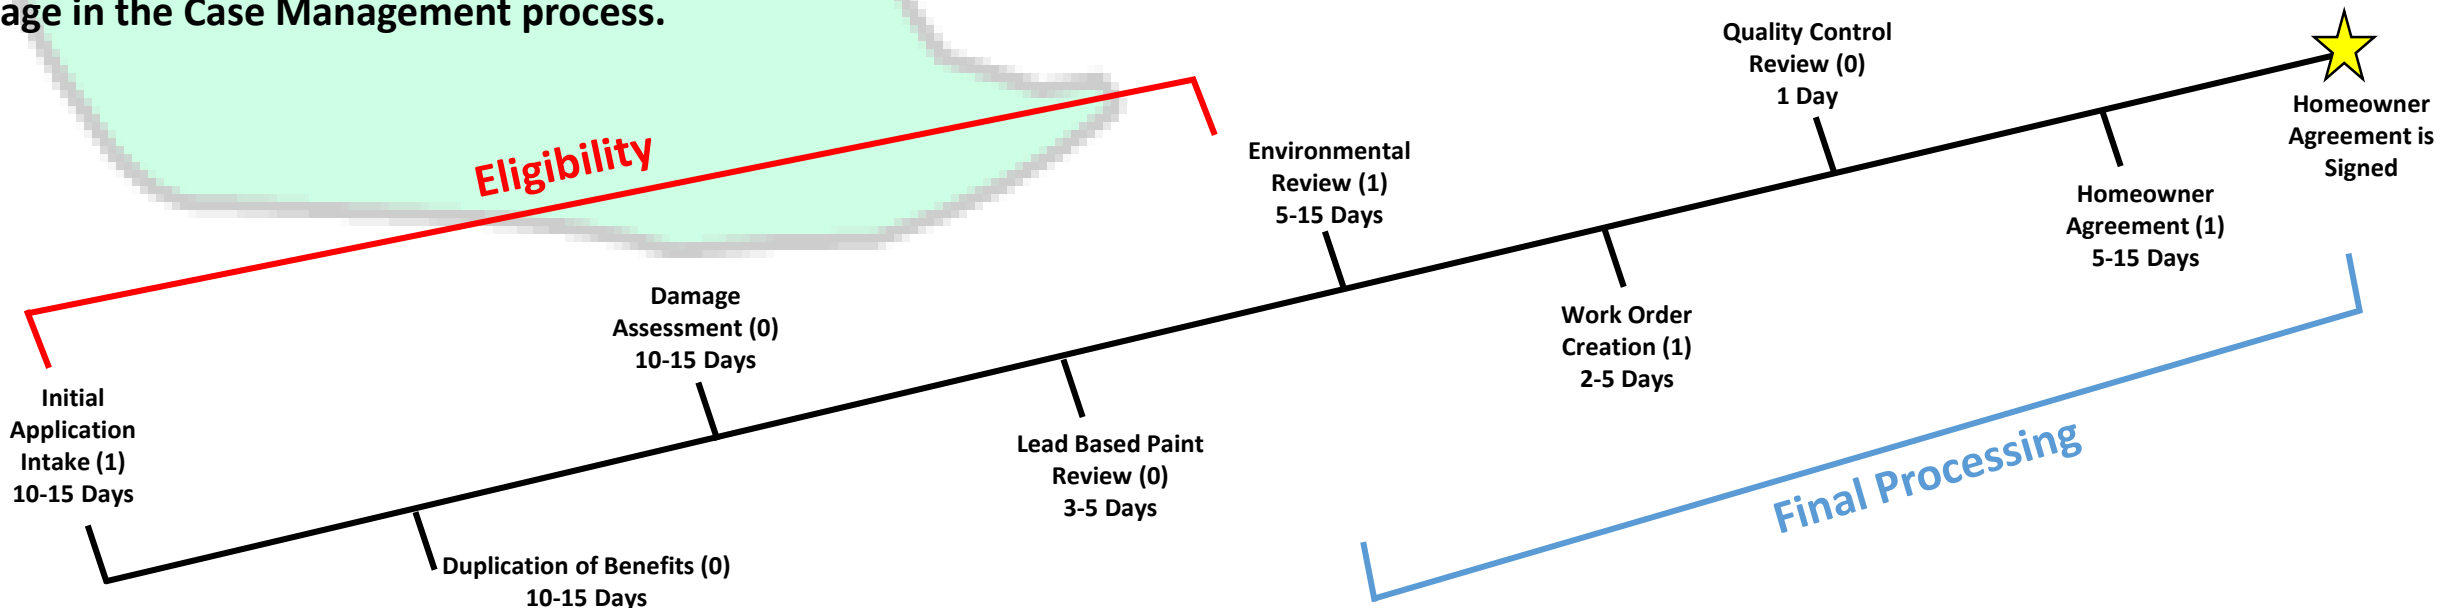


Lincoln County - Construction

Lincoln County currently has one (1) Cases in the early, or “Under Contract” stage of the Construction Process. The “Under Contract” stage consists of activities including; Receiving the Notification to Proceed, Construction Site Inspections, Permitting, and conducting Asbestos Inspections and Abatements.

Lincoln County also has zero (0) Cases in the “Active Construction” stage of the Construction Process. “Active Construction” consists of activities including; Removal and Replacement of Septic Systems, Demolition of Damaged Structure, and New Construction. This process concludes when all construction activities have been completed and the home has passed a Final Inspection certifying that it is ready for re-occupation by the Homeowner.

	CONSTRUCTION	TOTAL	COMPL
LINCOLN	RECONSTRUCTION	1	0
	REHABILITATION	0	0
	MHU	5	1
	UNASSIGNED	0	0
	TOTALS	6	1

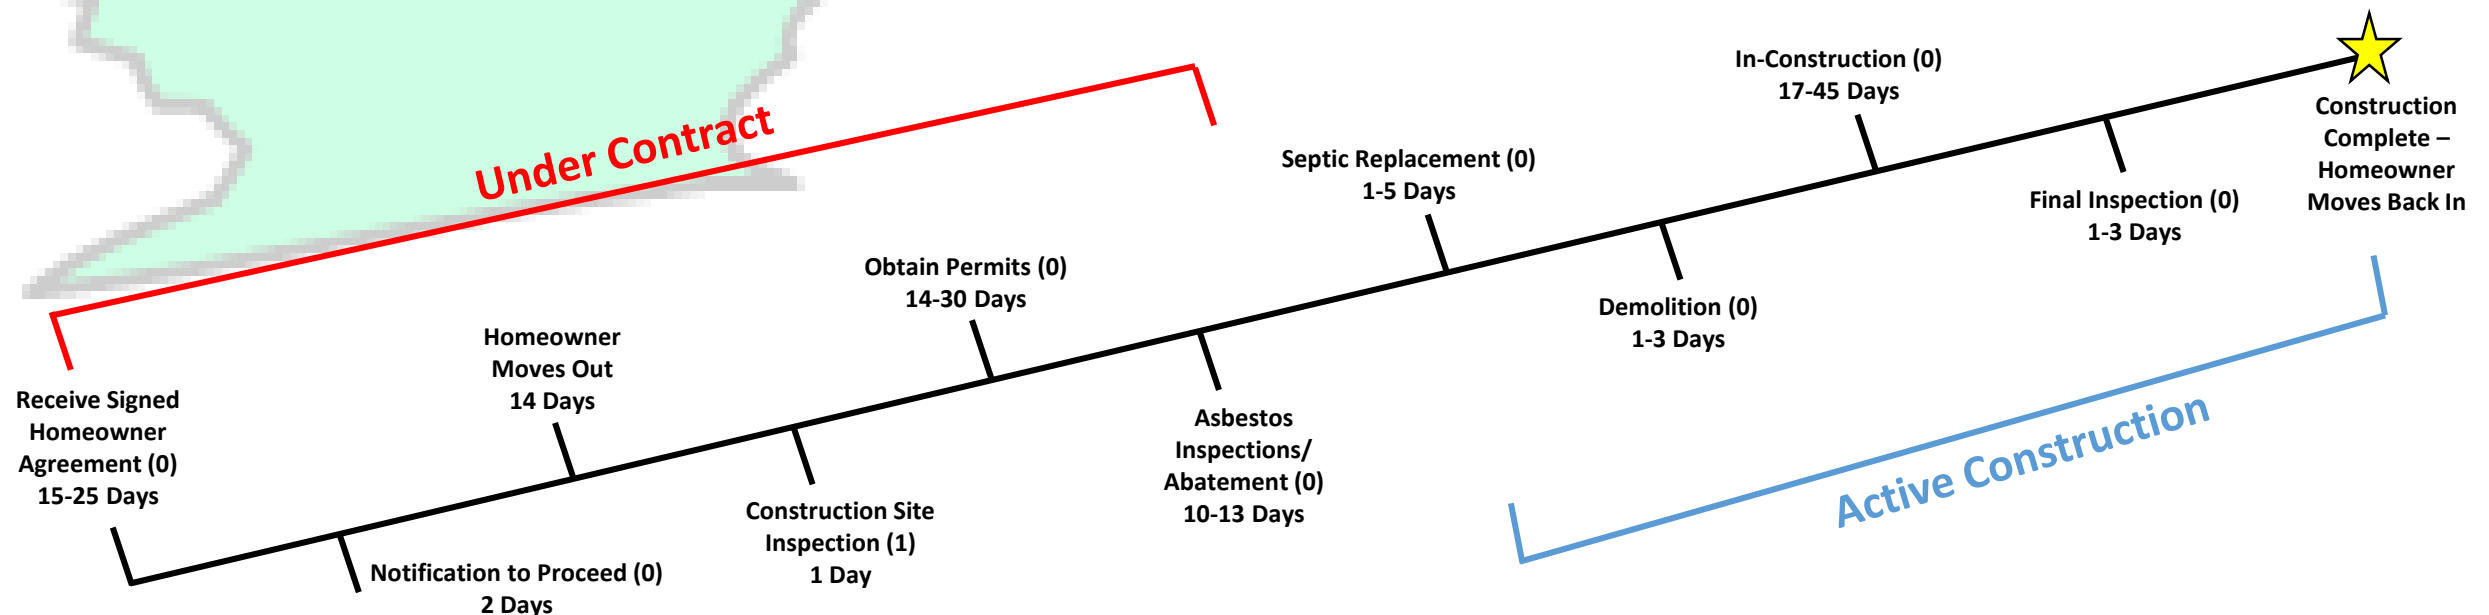


Lincoln County – Case Management

Case Managers continue to assist the Residents of Lincoln County by helping them through the “Eligibility” process. Currently, there are two (2) Cases going through the “Eligibility” process, which includes; Initial Application Intake, Damage Assessments to determine the type of work needed, Duplication of Benefits review, and testing for Lead Based Paints.

After “Eligibility” has been determined, Case Managers will begin the “Final Processing” of each Case file. Currently, Lincoln County has zero (3) going through this process, which includes the following activities; Environmental Reviews, construction Work Order development, and a Quality Control review. Once the Quality Control review is completed, the Case File will be ready for a Homeowner Agreement, which is the last stage in the Case Management process.

	CASE STATUS	TOTAL
LINCOLN	INITIAL INTAKE	0
	DAMAGE ASSESSMENT	2
	DOB REVIEW	0
	LBP REVIEW	0
	EHP / ERR REVIEW	3
	PACKET QA/QC	0
	WORK ORDER	0
	HOMEOWNER AGREEMENT	0
	PROCESS COMPLETE	1

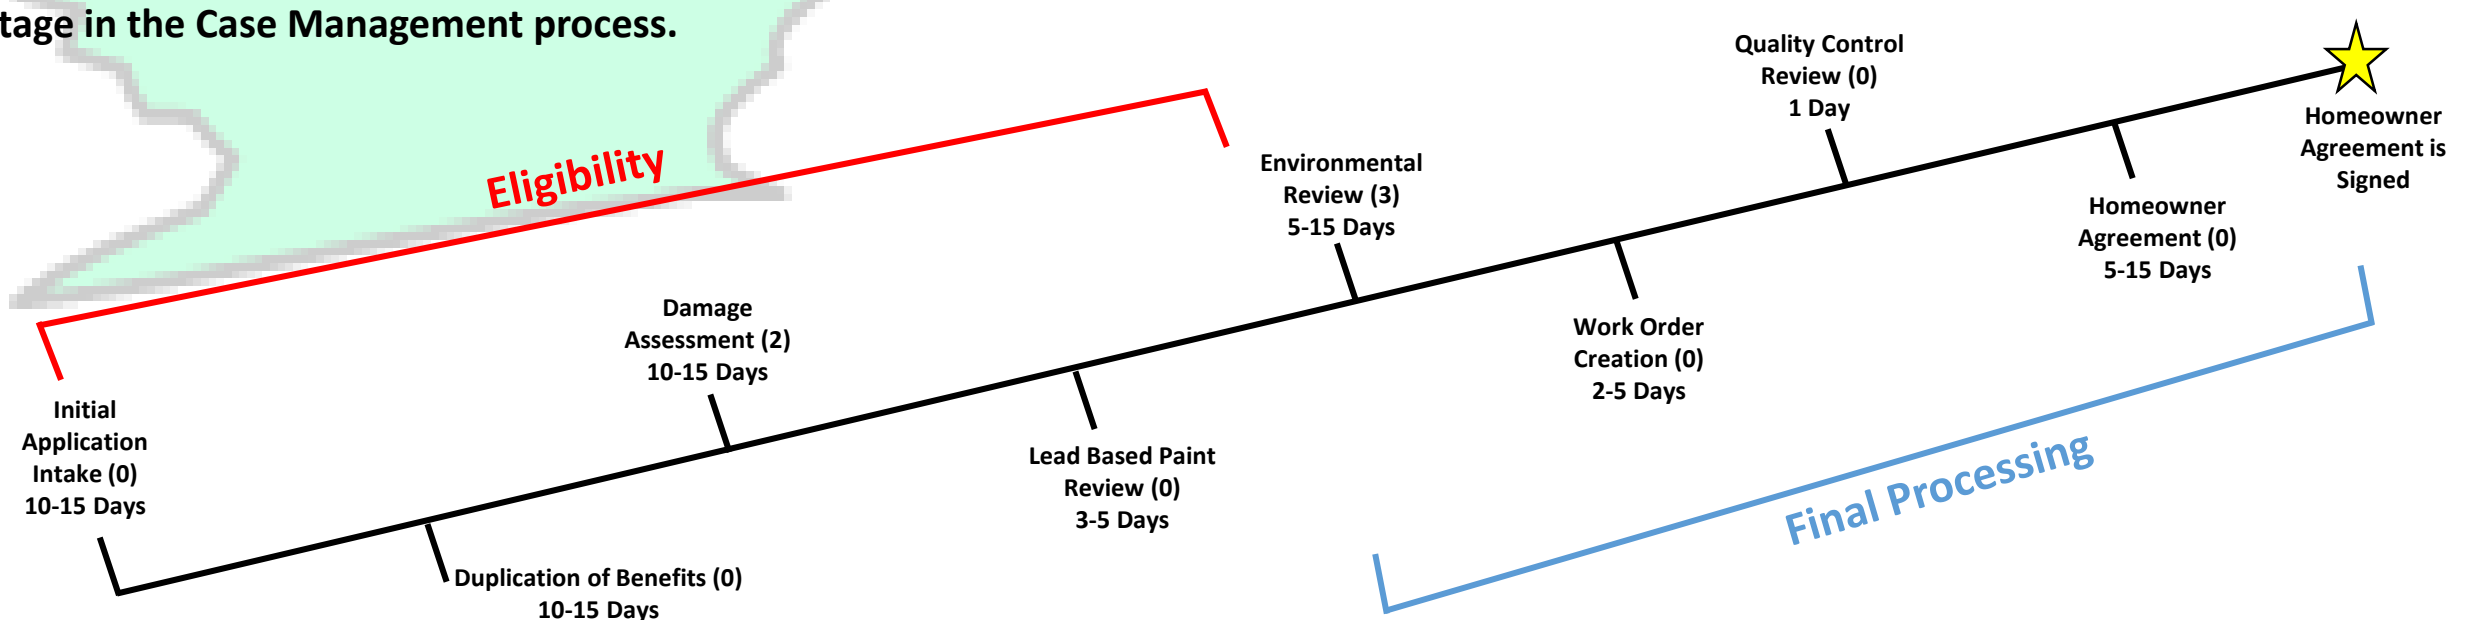


Monroe County - Construction

Monroe County currently has (1) Cases in the early, or “Under Contract” stage of the Construction Process. The “Under Contract” stage consists of activities including; Receiving the Notification to Proceed, Construction Site Inspections, Permitting, and conducting Asbestos Inspections and Abatements.

Monroe County also has two (0) Cases in the “Active Construction” stage of the Construction Process. “Active Construction” consists of activities including; Removal and Replacement of Septic Systems, Demolition of Damaged Structure, and New Construction. This process concludes when all construction activities have been completed and the home has passed a Final Inspection certifying that it is ready for re-occupation by the Homeowner.

	CONSTRUCTION	TOTAL	COMPL
MONROE	RECONSTRUCTION	2	0
	REHABILITATION	1	0
	MHU	0	0
	UNASSIGNED	0	0
	TOTALS	3	0

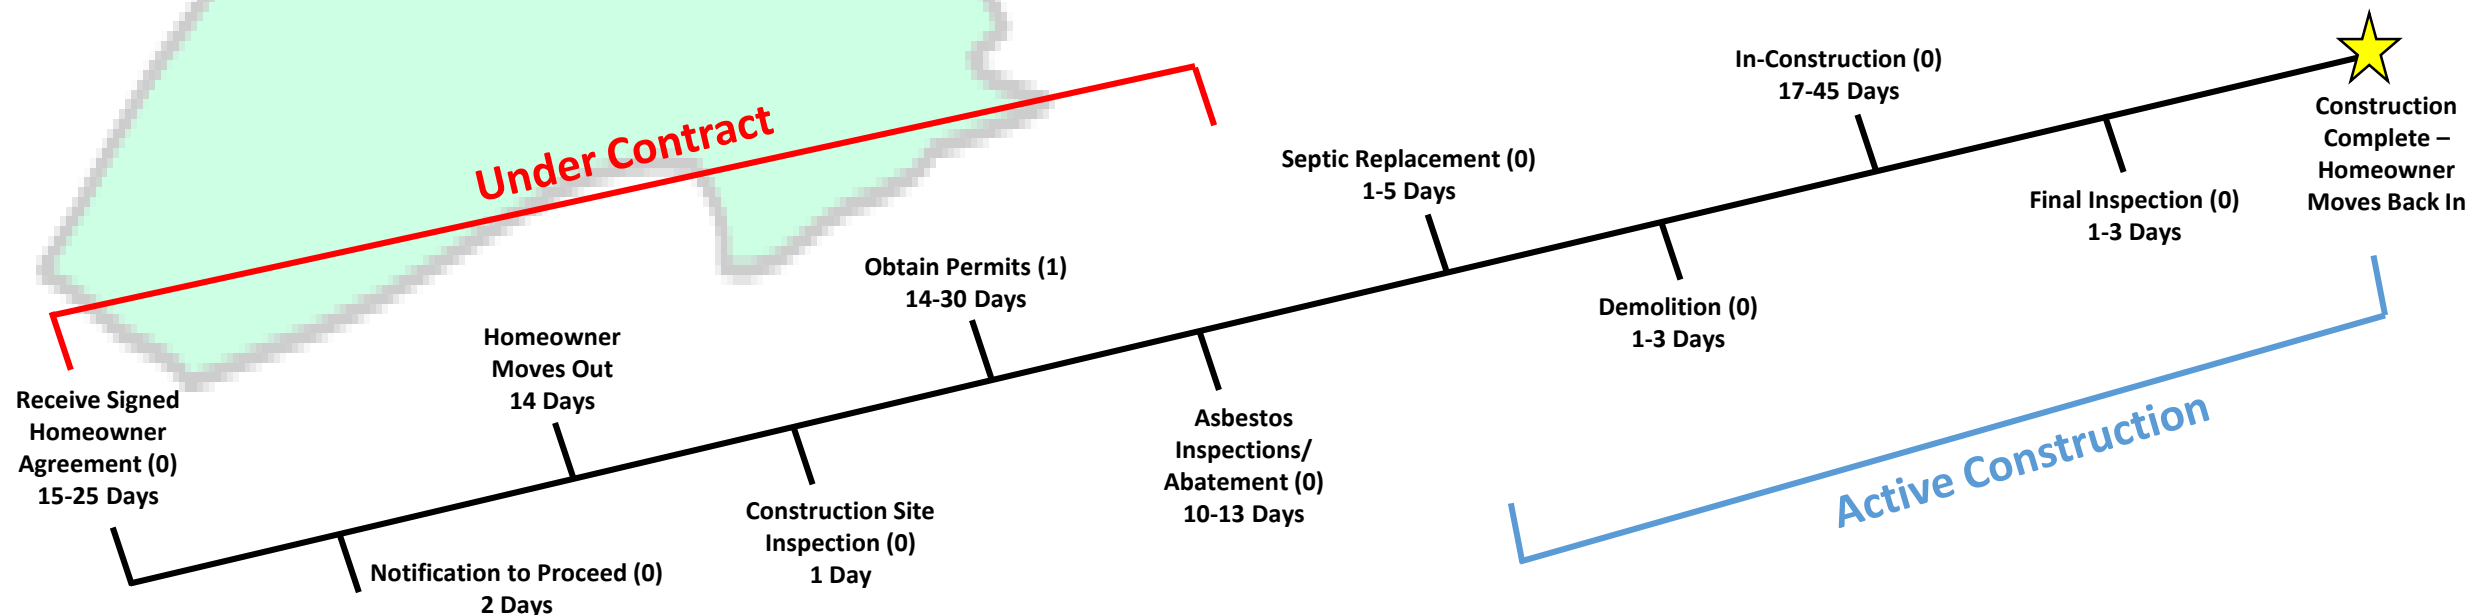


Monroe County – Case Management

Case Managers continue to assist the Residents of Monroe County by helping them through the “Eligibility” process. Currently, there are (1) Cases going through the “Eligibility” process, which includes; Initial Application Intake, Damage Assessments to determine the type of work needed, Duplication of Benefits review, and testing for Lead Based Paints.

After “Eligibility” has been determined, Case Managers will begin the “Final Processing” of each Case file. Currently, Monroe County has (1) going through this process, which includes the following activities; Environmental Reviews, construction Work Order development, and a Quality Control review. Once the Quality Control review is completed, the Case File will be ready for a Homeowner Agreement, which is the last stage in the Case Management process.

	CASE STATUS	TOTAL
MONROE	INITIAL INTAKE	1
	DAMAGE ASSESSMENT	0
	DOB REVIEW	0
	LBP REVIEW	0
	EHP / ERR REVIEW	1
	PACKET QA/QC	0
	WORK ORDER	0
	HOMEOWNER AGREEMENT	0
	PROCESS COMPLETE	1

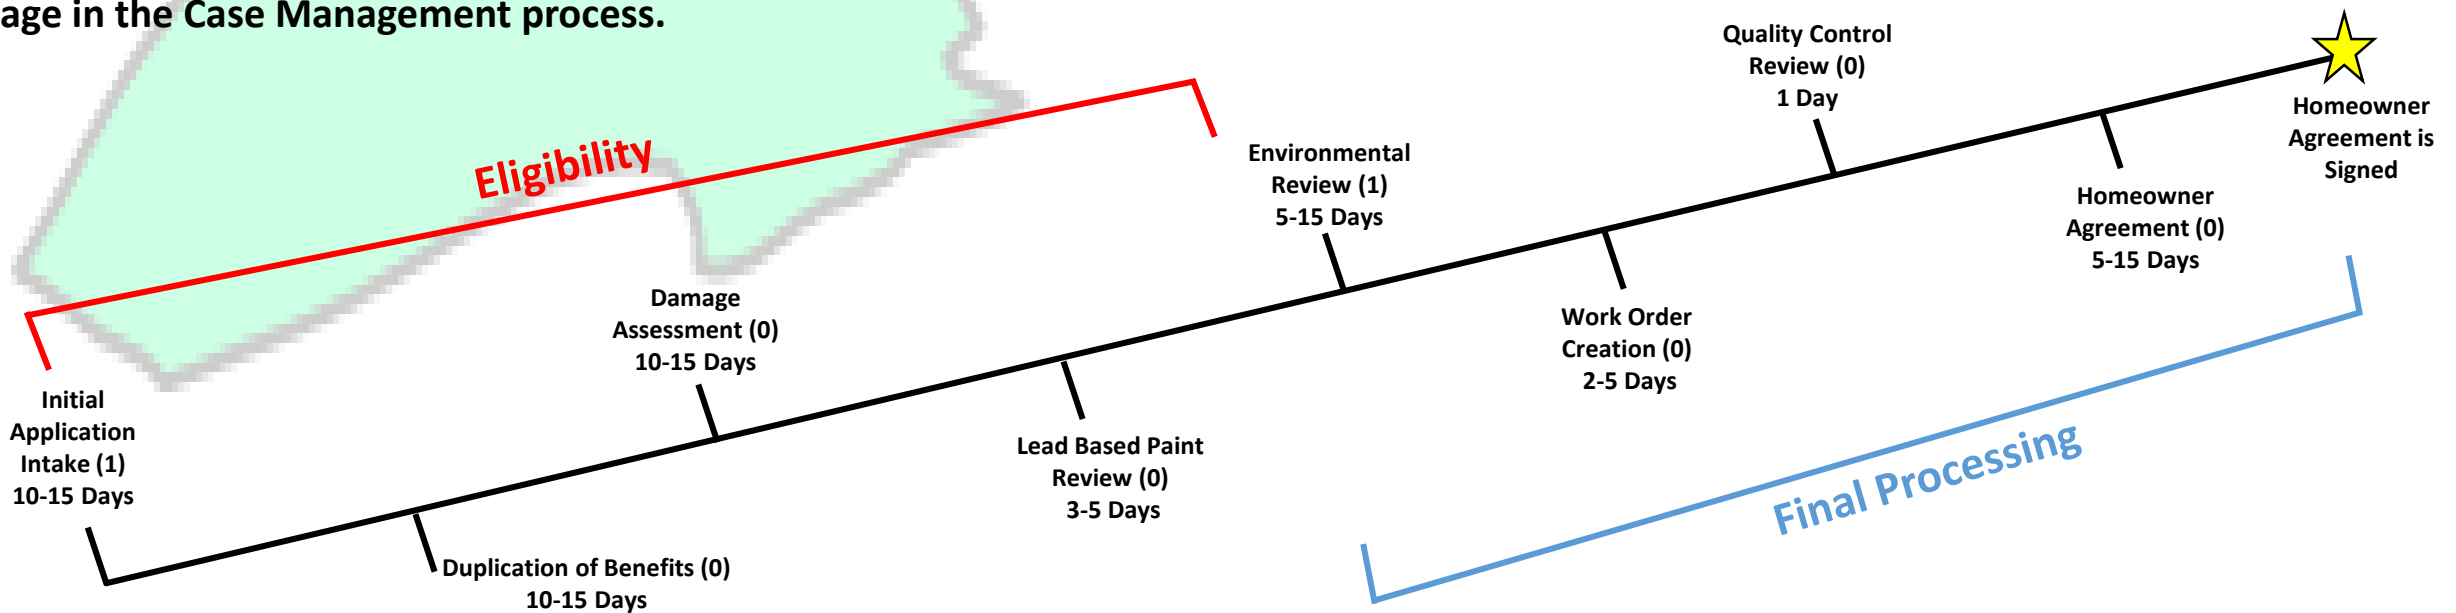


Summers County - Construction

Summers County currently has (1) Case in the early, or “Under Contract” stage of the Construction Process. The “Under Contract” stage consists of activities including; Receiving the Notification to Proceed, Construction Site Inspections, Permitting, and conducting Asbestos Inspections and Abatements.

Summers County also has (0) Cases in the “Active Construction” stage of the Construction Process. “Active Construction” consists of activities including; Removal and Replacement of Septic Systems, Demolition of Damaged Structure, and New Construction. This process concludes when all construction activities have been completed and the home has passed a Final Inspection certifying that it is ready for re-occupation by the Homeowner.

	CONSTRUCTION	TOTAL	COMPL
SUMMERS	RECONSTRUCTION	4	0
	REHABILITATION	2	0
	MHU	2	0
	UNASSIGNED	0	0
	TOTALS	8	0

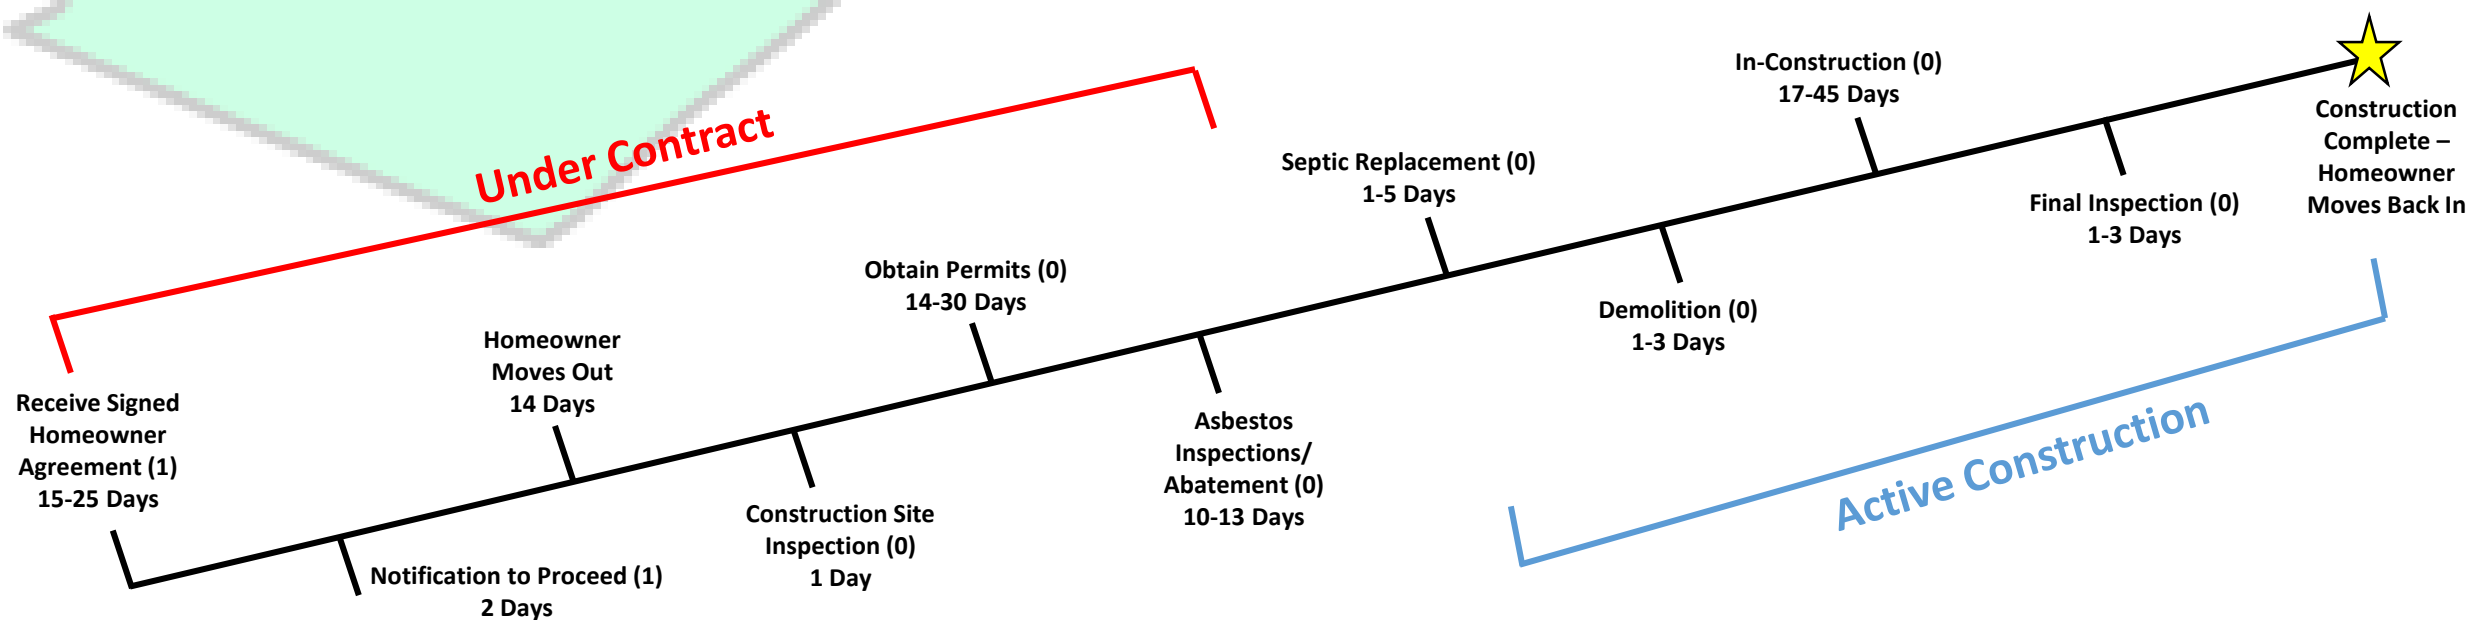


Summers County – Case Management

Case Managers continue to assist the Residents of Summers County by helping them through the “Eligibility” process. Currently, there are (3) Case going through the “Eligibility” process, which includes; Initial Application Intake, Damage Assessments to determine the type of work needed, Duplication of Benefits review, and testing for Lead Based Paints.

After “Eligibility” has been determined, Case Managers will begin the “Final Processing” of each Case file. Currently, Summers County has (4) going through this process, which includes the following activities; Environmental Reviews, construction Work Order development, and a Quality Control review. Once the Quality Control review is completed, the Case File will be ready for a Homeowner Agreement, which is the last stage in the Case Management process.

	CASE STATUS	TOTAL
SUMMERS	INITIAL INTAKE	1
	DAMAGE ASSESSMENT	1
	DOB REVIEW	0
	LBP REVIEW	1
	EHP / ERR REVIEW	0
	PACKET QA/QC	1
	WORK ORDER	2
	HOMEOWNER AGREEMENT	1
	PROCESS COMPLETE	8

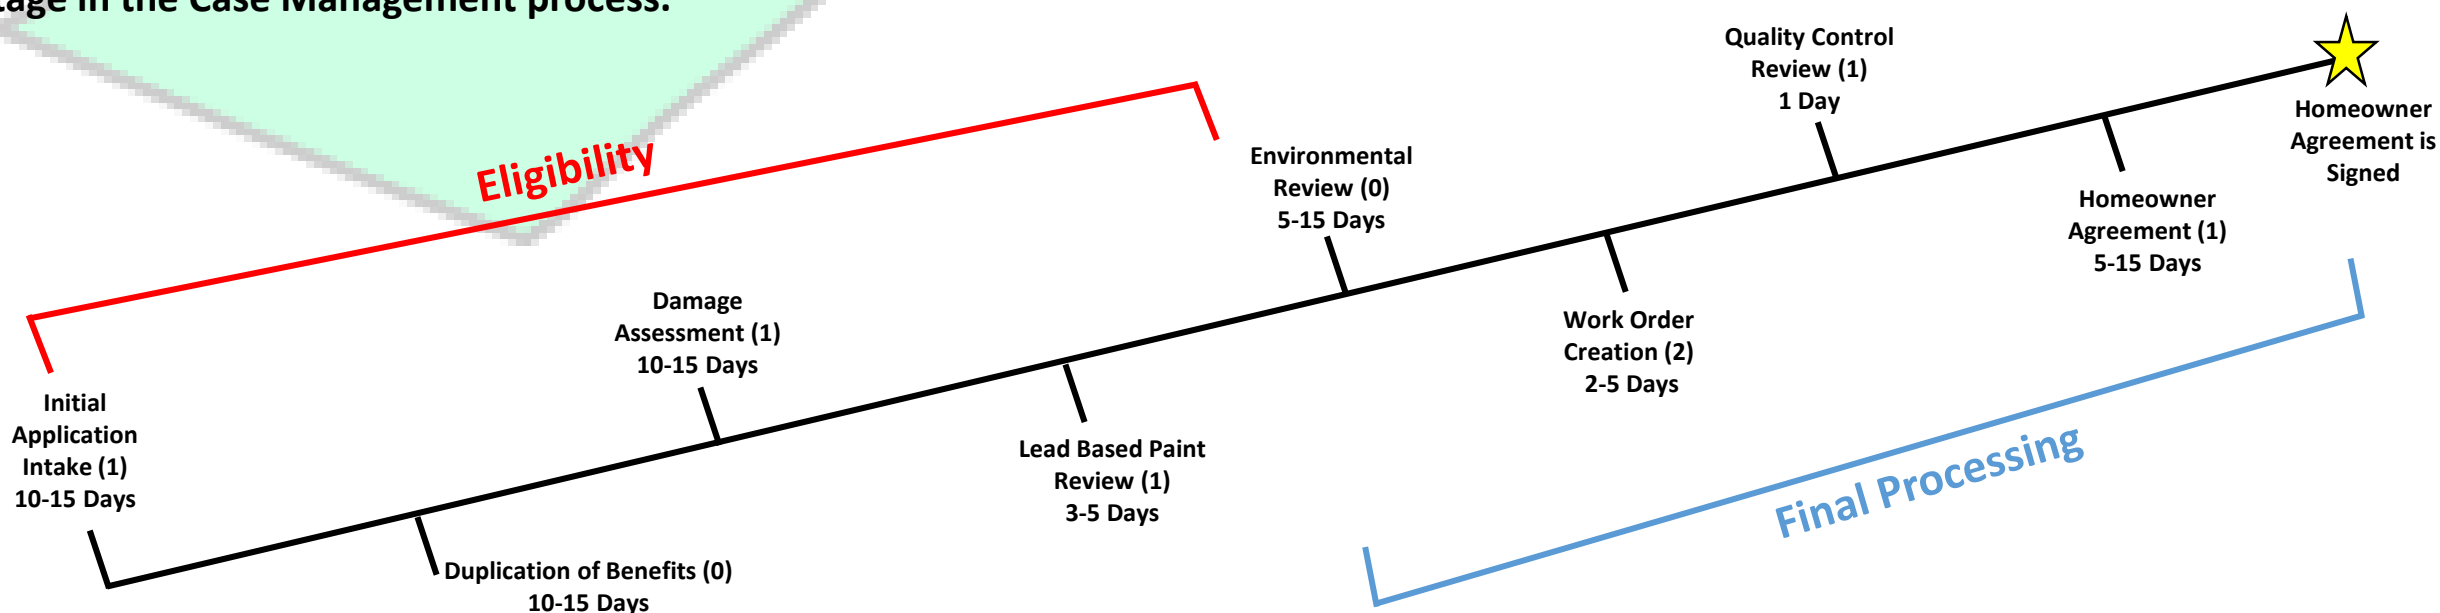


Webster County - Construction

Webster County currently has (3) Cases in the early, or “Under Contract” stage of the Construction Process. The “Under Contract” stage consists of activities including; Receiving the Notification to Proceed, Construction Site Inspections, Permitting, and conducting Asbestos Inspections and Abatements.

Webster County also has three (1) Cases in the “Active Construction” stage of the Construction Process. “Active Construction” consists of activities including; Removal and Replacement of Septic Systems, Demolition of Damaged Structure, and New Construction. This process concludes when all construction activities have been completed and the home has passed a Final Inspection certifying that it is ready for re-occupation by the Homeowner.

	CONSTRUCTION	TOTAL	COMPL
WEBSTER	RECONSTRUCTION	7	0
	REHABILITATION	6	0
	MHU	7	5
	UNASSIGNED	0	0
	TOTALS	20	5

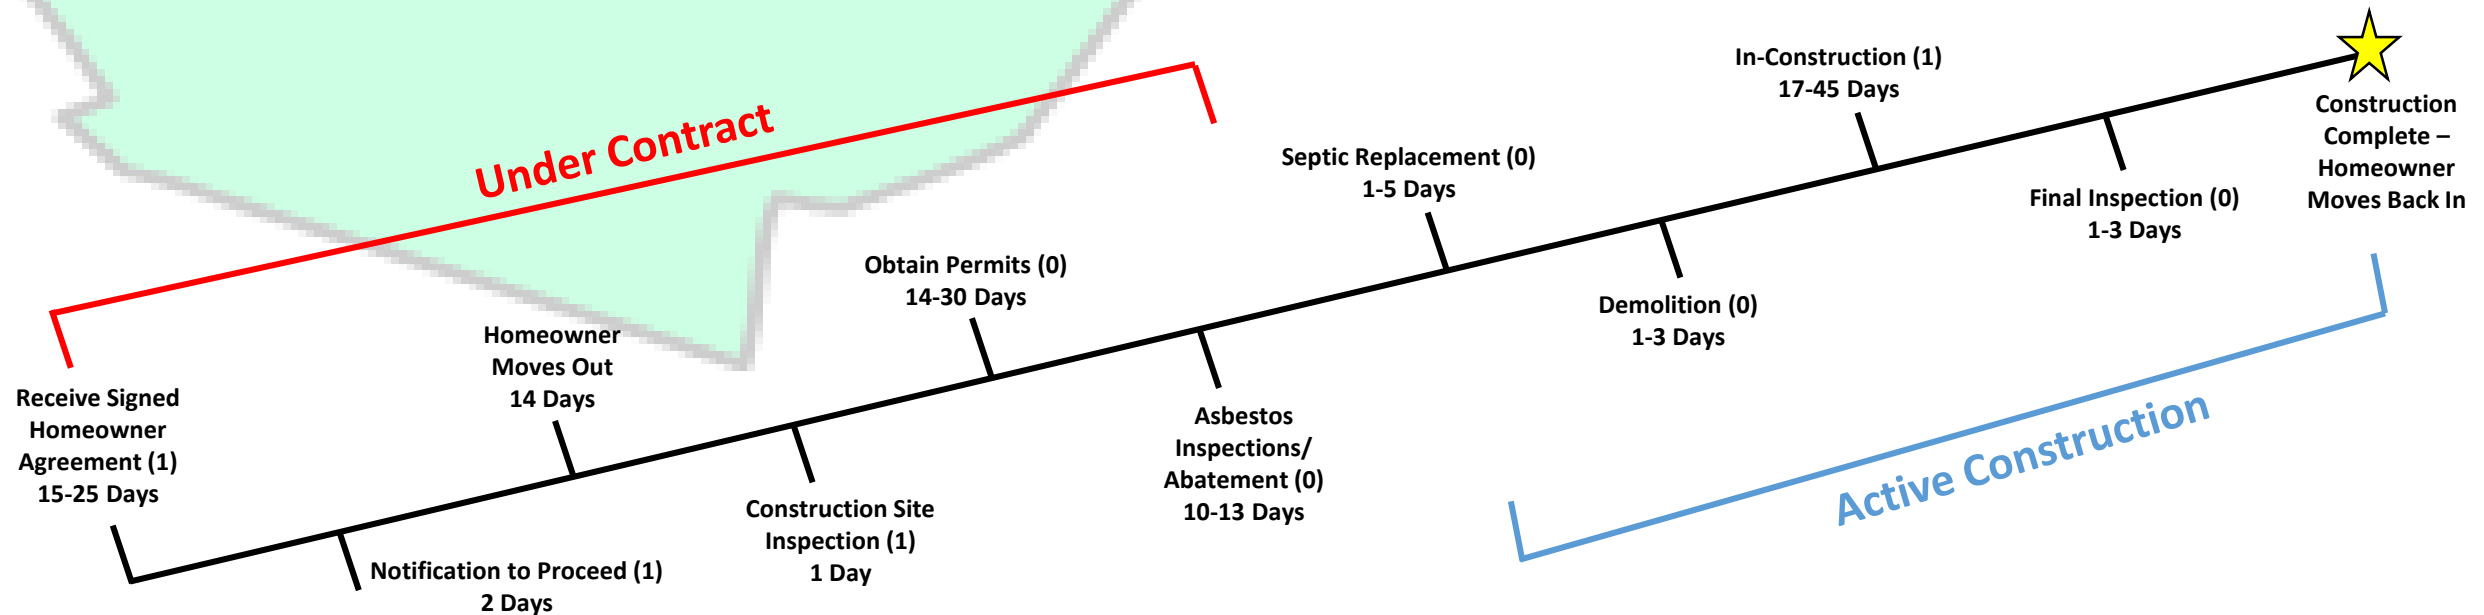


Webster County – Case Management

Case Managers continue to assist the Residents of Webster County by helping them through the “Eligibility” process. Currently, there are (10) Cases going through the “Eligibility” process, which includes; Initial Application Intake, Damage Assessments to determine the type of work needed, Duplication of Benefits review, and testing for Lead Based Paints.

After “Eligibility” has been determined, Case Managers will begin the “Final Processing” of each Case file. Currently, Webster County has (8) going through this process, which includes the following activities; Environmental Reviews, construction Work Order development, and a Quality Control review. Once the Quality Control review is completed, the Case File will be ready for a Homeowner Agreement, which is the last stage in the Case Management process.

	CASE STATUS	TOTAL
WEBSTER	INITIAL INTAKE	10
	DAMAGE ASSESSMENT	0
	DOB REVIEW	0
	LBP REVIEW	0
	EHP / ERR REVIEW	7
	PACKET QA/QC	0
	WORK ORDER	0
	HOMEOWNER AGREEMENT	1
	PROCESS COMPLETE	3

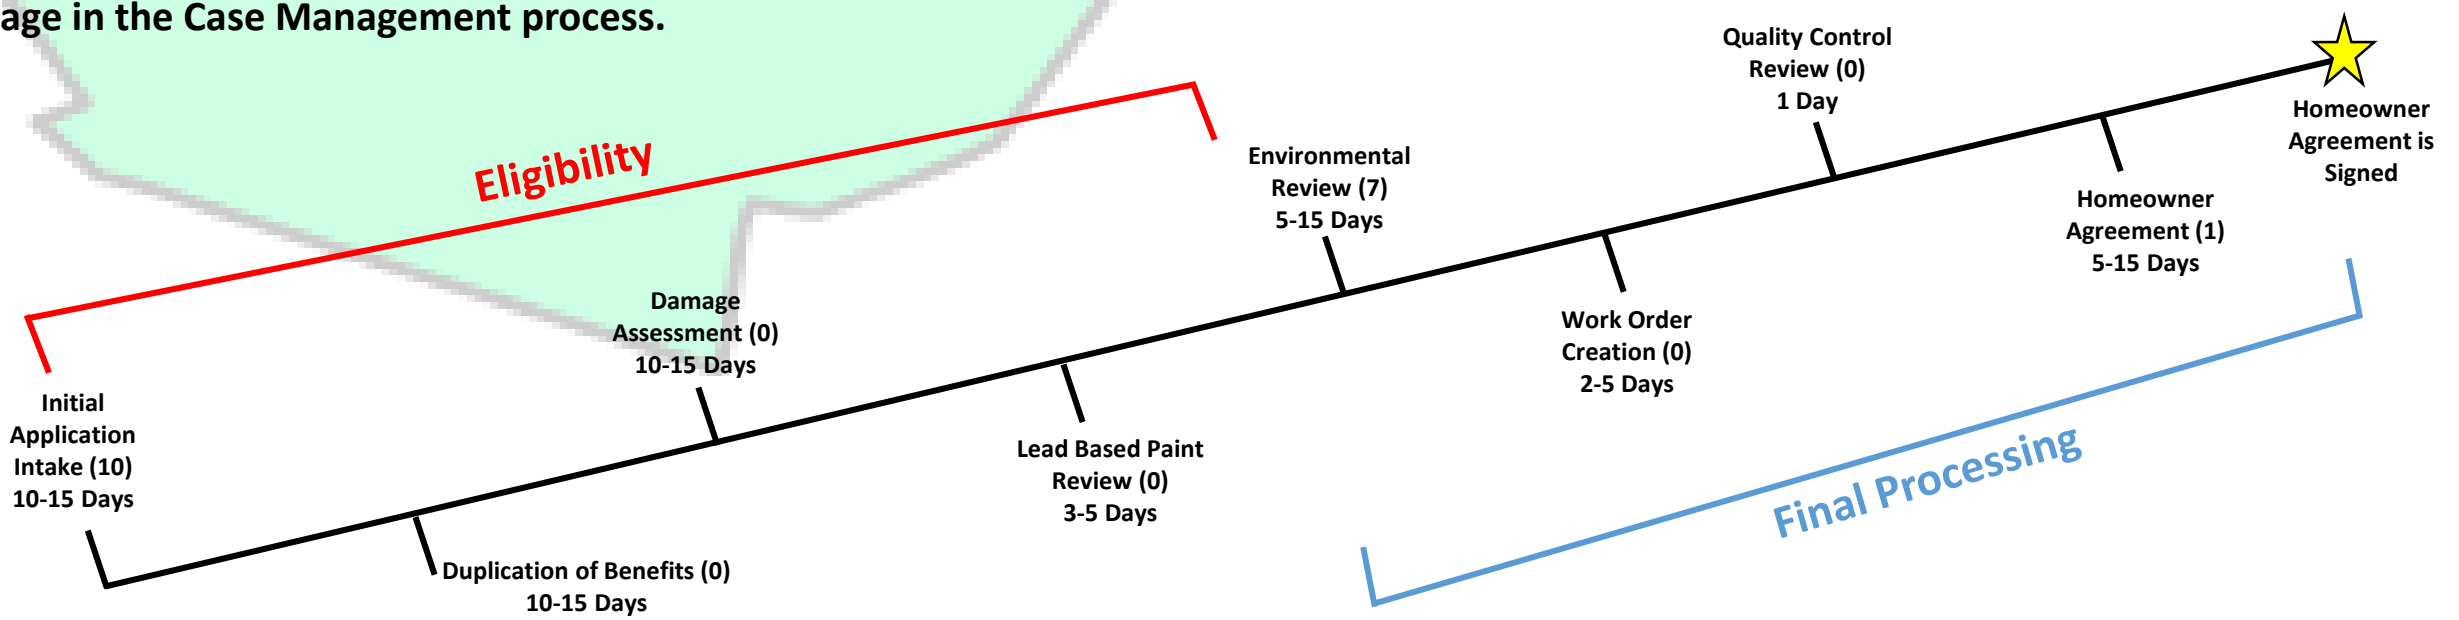


Pocahontas County - Construction

Pocahontas County currently has (2) Cases in the early, or “Under Contract” stage of the Construction Process. The “Under Contract” stage consists of activities including; Receiving the Notification to Proceed, Construction Site Inspections, Permitting, and conducting Asbestos Inspections and Abatements.

Pocahontas County also has three (0) Cases in the “Active Construction” stage of the Construction Process. “Active Construction” consists of activities including; Removal and Replacement of Septic Systems, Demolition of Damaged Structure, and New Construction. This process concludes when all construction activities have been completed and the home has passed a Final Inspection certifying that it is ready for re-occupation by the Homeowner.

	CONSTRUCTION	TOTAL	COMPL
POCAHONTAS	RECONSTRUCTION	1	0
	REHABILITATION	1	0
	MHU	1	0
	UNASSIGNED	0	0
	TOTALS	3	0

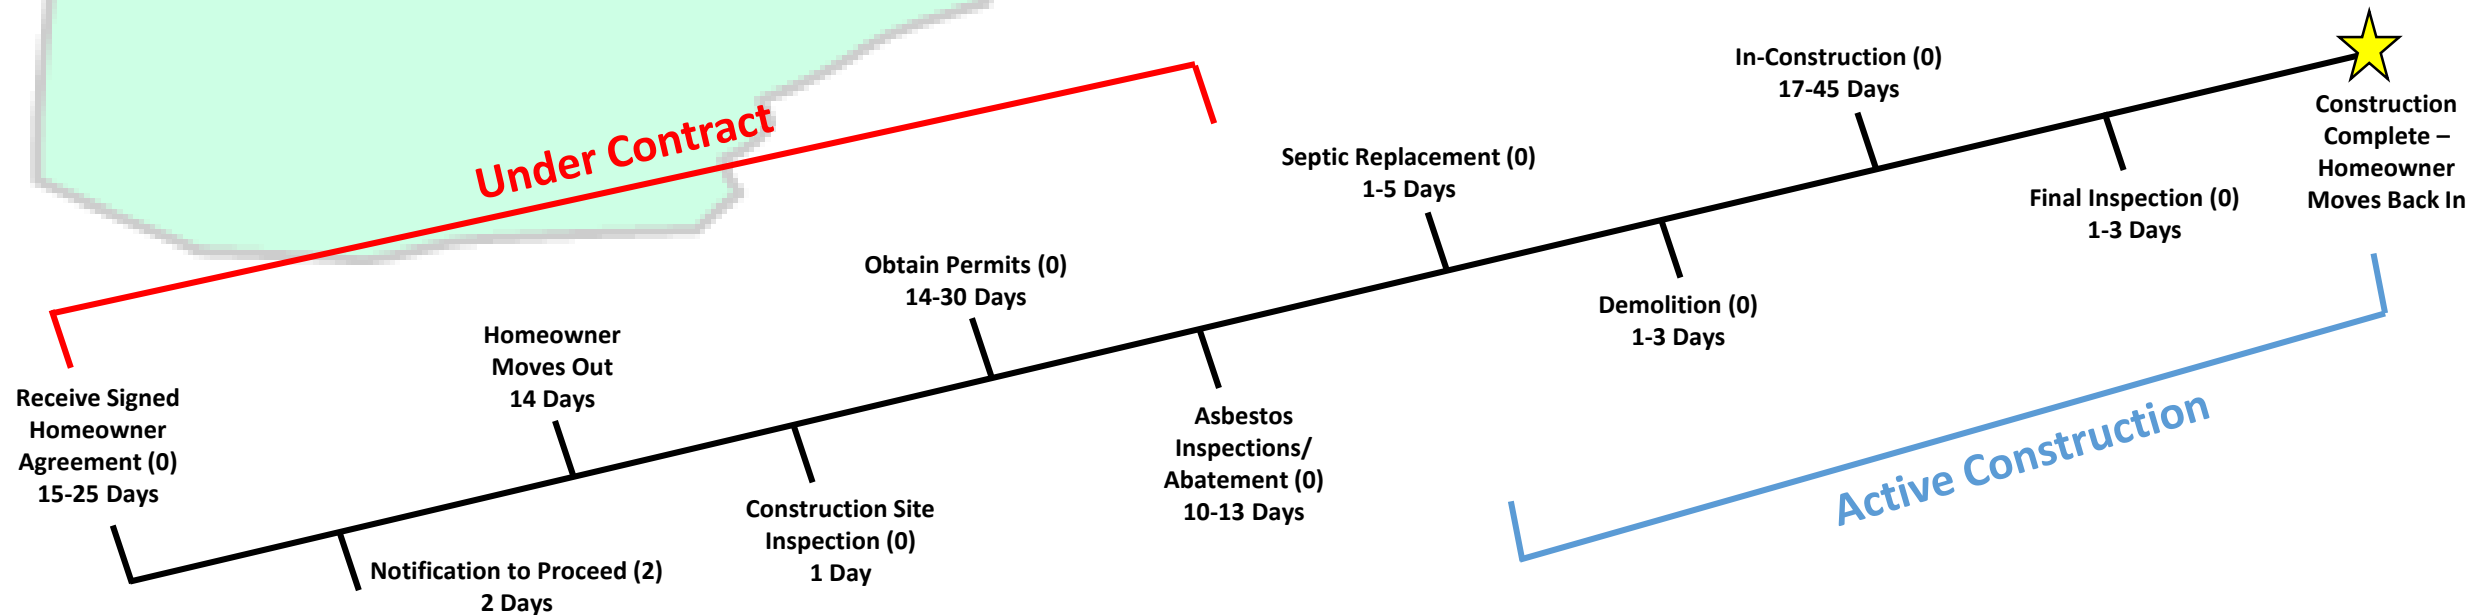

Pocahontas County – Case Management

Case Managers continue to assist the Residents of Pocahontas County by helping them through the “Eligibility” process. Currently, there are (1) Cases going through the “Eligibility” process, which includes; Initial Application Intake, Damage Assessments to determine the type of work needed, Duplication of Benefits review, and testing for Lead Based Paints.

After “Eligibility” has been determined, Case Managers will begin the “Final Processing” of each Case file. Currently, Pocahontas County has (0) going through this process, which includes the following activities; Environmental Reviews, construction Work Order development, and a Quality Control review. Once the Quality Control review is completed, the Case File will be ready for a Homeowner Agreement, which is the last stage in the Case Management process.

	CASE STATUS	TOTAL
POCAHONTAS	INITIAL INTAKE	1
	DAMAGE ASSESSMENT	0
	DOB REVIEW	0
	LBP REVIEW	0
	EHP / ERR REVIEW	0
	PACKET QA/QC	0
	WORK ORDER	0
	HOMEOWNER AGREEMENT	0
	PROCESS COMPLETE	2

